
PROGRAMME OF WORKS: IKEJA CORPORATE OFFICE


Demo Partners QS Contract period: 11 January 2027 to 29 February 2028 (14 months) Monday to Saturday, Nigerian public holidays excluded Revision B, 02 November 2026

Critical With float


ID	Task Name	Duration	Start	Finish	Predecessors
1	**PROGRAMME OF WORKS**	**349 days**	**11 Jan 2027**	**29 Feb 2028**	
2	**KEY DATES**	**1 day**	**11 Jan 2027**	**11 Jan 2027**	
3	**Letter of award**	**0 days**	**11 Jan 2027**	**11 Jan 2027**	
4	**Site possession and handover of site**	**0 days**	**11 Jan 2027**	**11 Jan 2027**	**3**
5	**PRELIMINARIES AND MOBILISATION**	**20 days**	**11 Jan 2027**	**02 Feb 2027**	
6	Mobilisation of personnel and equipment	10 days	11 Jan 2027	21 Jan 2027	4
7	Site clearance	6 days	13 Jan 2027	19 Jan 2027	6SS+2
8	Hoarding, gates and site security	8 days	15 Jan 2027	23 Jan 2027	7SS+2
9	Site offices, stores and welfare facilities	10 days	18 Jan 2027	28 Jan 2027	8SS+2
10	Temporary water and power supply	5 days	22 Jan 2027	27 Jan 2027	9SS+4
11	Setting out and survey of building lines	4 days	28 Jan 2027	01 Feb 2027	10
12	Approval of setting out by the consultant	1 day	02 Feb 2027	02 Feb 2027	11
13	**PROCUREMENT**	**45 days**	**11 Jan 2027**	**03 Mar 2027**	
14	Structural steel: shop drawings	10 days	11 Jan 2027	21 Jan 2027	4
15	Structural steel: consultant approval	5 days	22 Jan 2027	27 Jan 2027	14
16	Roofing materials: samples and approval	5 days	11 Jan 2027	15 Jan 2027	4
17	Roofing materials: delivery to site	15 days	16 Jan 2027	02 Feb 2027	16
18	Windows and glazing: shop drawings	10 days	11 Jan 2027	21 Jan 2027	4
19	Windows and glazing: consultant approval	5 days	22 Jan 2027	27 Jan 2027	18
20	Windows and glazing: manufacture and delivery	30 days	28 Jan 2027	03 Mar 2027	19
21	Doors and ironmongery: schedule approval	5 days	11 Jan 2027	15 Jan 2027	4
22	Doors and ironmongery: manufacture and delivery	25 days	16 Jan 2027	13 Feb 2027	21
23	Ceiling materials: samples and approval	5 days	11 Jan 2027	15 Jan 2027	4
24	Ceiling materials: delivery to site	15 days	16 Jan 2027	02 Feb 2027	23
25	Electrical boards and fittings: submittals and approval	10 days	11 Jan 2027	21 Jan 2027	4
26	Electrical boards and fittings: delivery to site	30 days	22 Jan 2027	25 Feb 2027	25
27	**SUBSTRUCTURE**	**43 days**	**03 Feb 2027**	**24 Mar 2027**	
28	**GROUND FLOOR**	**17 days**	**05 Mar 2027**	**24 Mar 2027**	
29	Reinforcement to foundations and ground slab, Ground Floor	5 days	05 Mar 2027	10 Mar 2027	48
30	Formwork to foundations and ground slab, Ground Floor	5 days	08 Mar 2027	12 Mar 2027	29SS+2
31	Inspection and approval of reinforcement, Ground Floor	5 days	10 Mar 2027	15 Mar 2027	30SS+2
32	Concrete placement to foundations and ground slab, Ground Floor	5 days	12 Mar 2027	17 Mar 2027	31SS+2
33	Curing and striking of formwork to foundations and ground slab, Ground F...	5 days	15 Mar 2027	19 Mar 2027	32SS+2
34	Substructure	4 days	20 Mar 2027	24 Mar 2027	33
35	**WHOLE BUILDING**	**26 days**	**03 Feb 2027**	**04 Mar 2027**	
36	Excavation to reduced levels and foundation trenches	2 days	03 Feb 2027	04 Feb 2027	12

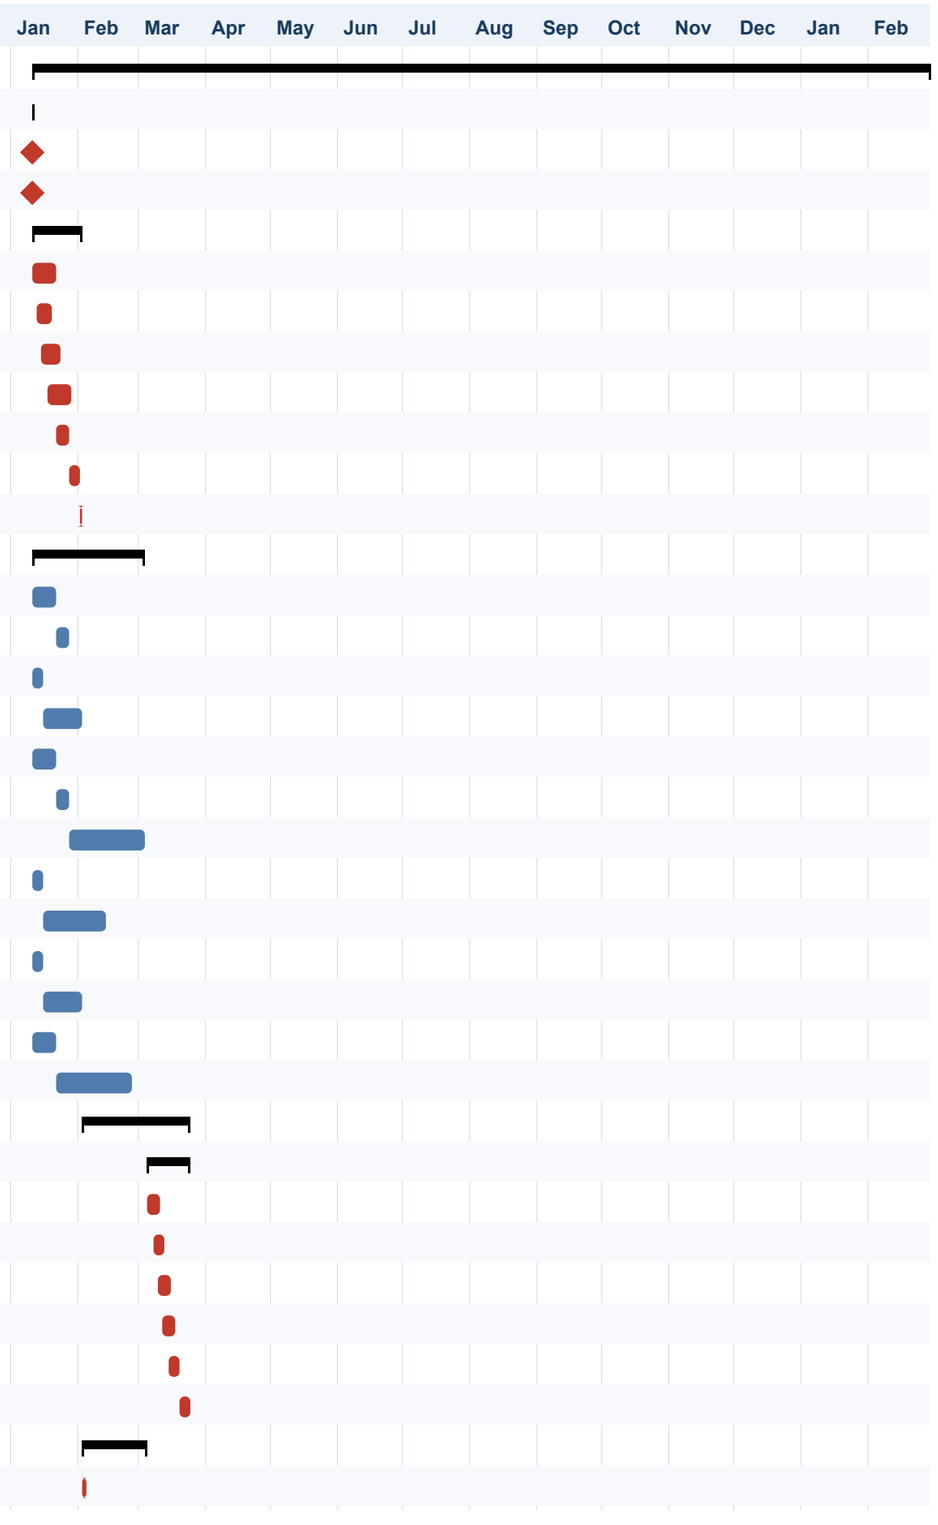

ID	Task Name	Duration	Start	Finish	Predecessors
37	Disposal of excavated material	2 days	04 Feb 2027	05 Feb 2027	36SS+1
38	Formwork to foundations and ground slab	4 days	06 Feb 2027	10 Feb 2027	37
39	Reinforcement to foundations and ground slab	2 days	06 Feb 2027	08 Feb 2027	37
40	Inspection and approval of reinforcement	2 days	08 Feb 2027	09 Feb 2027	39SS+1
41	Reinforcement to foundations and ground slab	1 day	11 Feb 2027	11 Feb 2027	40, 38
42	Formwork to foundations and ground slab	1 day	12 Feb 2027	12 Feb 2027	41SS+1
43	Inspection and approval of reinforcement	1 day	13 Feb 2027	13 Feb 2027	42SS+1
44	Concrete placement to foundations and ground slab	1 day	15 Feb 2027	15 Feb 2027	43SS+1
45	Curing and striking of formwork to foundations and ground slab	1 day	16 Feb 2027	16 Feb 2027	44SS+1
46	Backfilling and compaction	2 days	17 Feb 2027	18 Feb 2027	45
47	Hardcore filling and blinding	2 days	18 Feb 2027	19 Feb 2027	46SS+1
48	Anti-termite treatment and damp-proof membrane	11 days	20 Feb 2027	04 Mar 2027	47
49	**SUPERSTRUCTURE**	**49 days**	**25 Mar 2027**	**24 May 2027**	
50	**GROUND FLOOR**	**40 days**	**25 Mar 2027**	**13 May 2027**	
51	Fabrication and delivery of structural steel, Ground Floor	5 days	25 Mar 2027	01 Apr 2027	15, 34
52	Erection of steel columns, Ground Floor	5 days	30 Mar 2027	03 Apr 2027	51SS+2
53	Erection of steel beams and joists, Ground Floor	5 days	01 Apr 2027	06 Apr 2027	52SS+2
54	Bolting, plumbing and final tightening, Ground Floor	5 days	03 Apr 2027	08 Apr 2027	53SS+2
55	Reinforcement to columns and beams, Ground Floor	4 days	09 Apr 2027	13 Apr 2027	54
56	Formwork to columns and beams, Ground Floor	4 days	10 Apr 2027	14 Apr 2027	55SS+1
57	Inspection and approval of reinforcement, Ground Floor	4 days	12 Apr 2027	15 Apr 2027	56SS+1
58	Concrete placement to columns and beams, Ground Floor	4 days	13 Apr 2027	16 Apr 2027	57SS+1
59	Curing and striking of formwork to columns and beams, Ground Floor	4 days	14 Apr 2027	17 Apr 2027	58SS+1
60	Steel stair stringers and treads, Ground Floor	4 days	19 Apr 2027	22 Apr 2027	59
61	Reinforcement to staircase, Ground Floor	1 day	23 Apr 2027	23 Apr 2027	60
62	Formwork to staircase, Ground Floor	1 day	24 Apr 2027	24 Apr 2027	61SS+1
63	Inspection and approval of reinforcement, Ground Floor	1 day	26 Apr 2027	26 Apr 2027	62SS+1
64	Concrete placement to staircase, Ground Floor	1 day	27 Apr 2027	27 Apr 2027	63SS+1
65	Curing and striking of formwork to staircase, Ground Floor	1 day	28 Apr 2027	28 Apr 2027	64SS+1
66	Balustrades and handrails to stairs, Ground Floor	12 days	29 Apr 2027	13 May 2027	65
67	**FIRST FLOOR**	**30 days**	**19 Apr 2027**	**24 May 2027**	
68	Fabrication and delivery of structural steel, First Floor	1 day	19 Apr 2027	19 Apr 2027	59, 34
69	Erection of steel columns, First Floor	1 day	20 Apr 2027	20 Apr 2027	68SS+1
70	Erection of steel beams and joists, First Floor	1 day	21 Apr 2027	21 Apr 2027	69SS+1
71	Bolting, plumbing and final tightening, First Floor	1 day	22 Apr 2027	22 Apr 2027	70SS+1
72	Reinforcement to columns and beams, First Floor	1 day	23 Apr 2027	23 Apr 2027	71

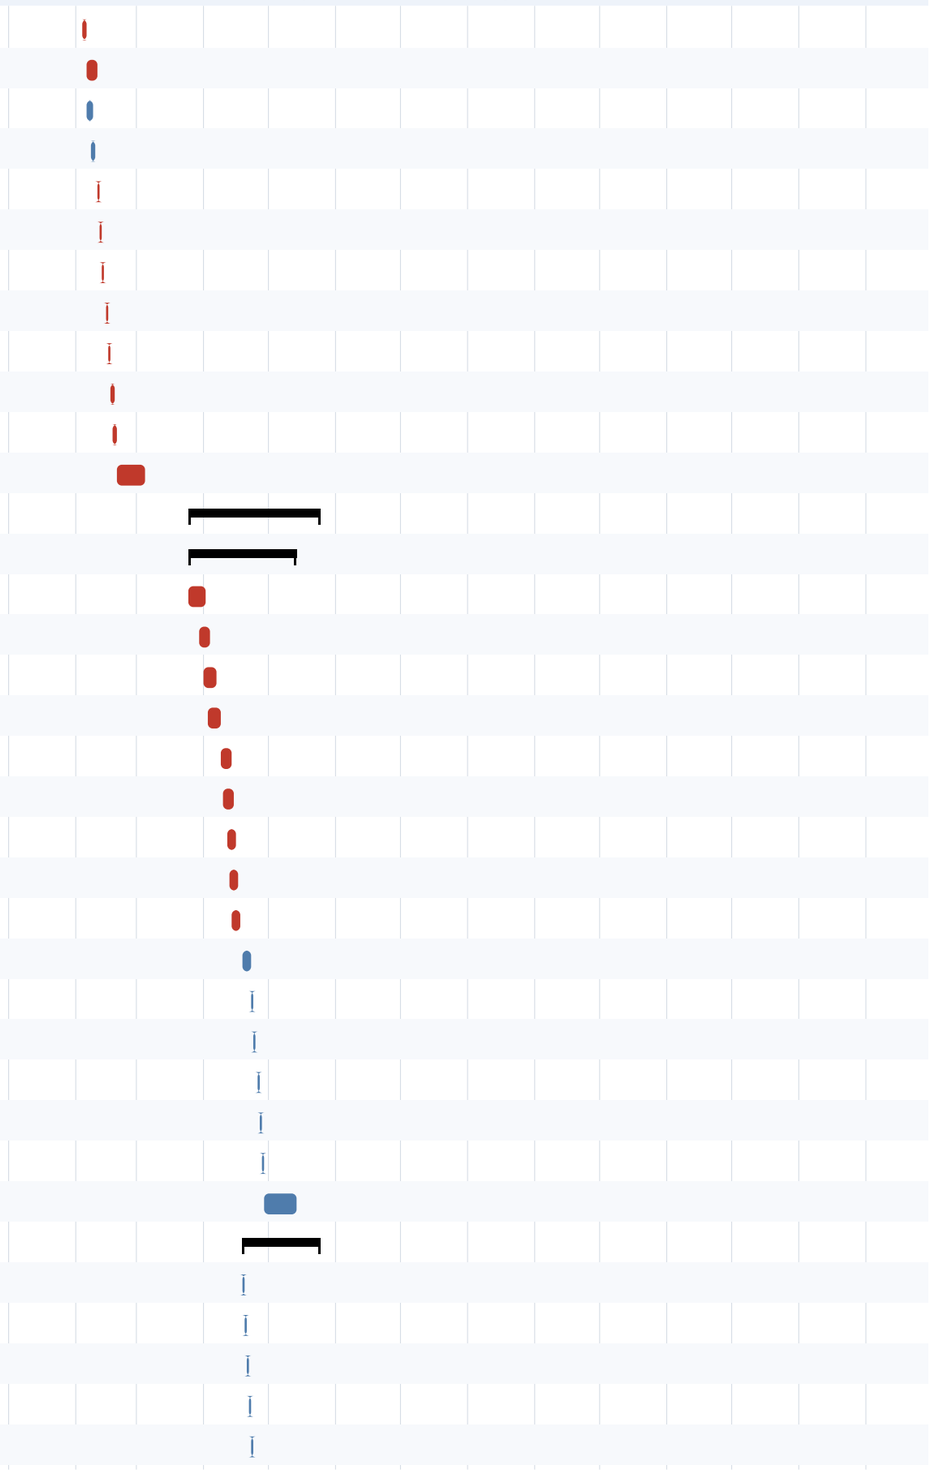

ID	Task Name	Duration	Start	Finish	Predecessors
73	Formwork to columns and beams, First Floor	1 day	24 Apr 2027	24 Apr 2027	72SS+1
74	Inspection and approval of reinforcement, First Floor	1 day	26 Apr 2027	26 Apr 2027	73SS+1
75	Concrete placement to columns and beams, First Floor	1 day	27 Apr 2027	27 Apr 2027	74SS+1
76	Curing and striking of formwork to columns and beams, First Floor	1 day	28 Apr 2027	28 Apr 2027	75SS+1
77	Reinforcement to suspended slab, First Floor	1 day	19 Apr 2027	19 Apr 2027	59
78	Formwork to suspended slab, First Floor	1 day	20 Apr 2027	20 Apr 2027	77SS+1
79	Inspection and approval of reinforcement, First Floor	1 day	21 Apr 2027	21 Apr 2027	78SS+1
80	Concrete placement to suspended slab, First Floor	1 day	22 Apr 2027	22 Apr 2027	79SS+1
81	Curing and striking of formwork to suspended slab, First Floor	1 day	23 Apr 2027	23 Apr 2027	80SS+1
82	Steel stair stringers and treads, First Floor	4 days	29 Apr 2027	04 May 2027	81, 76
83	Reinforcement to staircase, First Floor	4 days	05 May 2027	08 May 2027	82
84	Formwork to staircase, First Floor	4 days	06 May 2027	10 May 2027	83SS+1
85	Inspection and approval of reinforcement, First Floor	4 days	07 May 2027	11 May 2027	84SS+1
86	Concrete placement to staircase, First Floor	4 days	08 May 2027	12 May 2027	85SS+1
87	Curing and striking of formwork to staircase, First Floor	4 days	10 May 2027	13 May 2027	86SS+1
88	Balustrades and handrails to stairs, First Floor	9 days	14 May 2027	24 May 2027	87
89	**SECOND FLOOR**	**14 days**	**29 Apr 2027**	**15 May 2027**	
90	Reinforcement to columns and beams, Second Floor	1 day	29 Apr 2027	29 Apr 2027	34, 76
91	Formwork to columns and beams, Second Floor	1 day	30 Apr 2027	30 Apr 2027	90SS+1
92	Inspection and approval of reinforcement, Second Floor	1 day	03 May 2027	03 May 2027	91SS+1
93	Concrete placement to columns and beams, Second Floor	1 day	04 May 2027	04 May 2027	92SS+1
94	Curing and striking of formwork to columns and beams, Second Floor	1 day	05 May 2027	05 May 2027	93SS+1
95	Reinforcement to suspended slab, Second Floor	1 day	29 Apr 2027	29 Apr 2027	76
96	Formwork to suspended slab, Second Floor	1 day	30 Apr 2027	30 Apr 2027	95SS+1
97	Inspection and approval of reinforcement, Second Floor	1 day	03 May 2027	03 May 2027	96SS+1
98	Concrete placement to suspended slab, Second Floor	1 day	04 May 2027	04 May 2027	97SS+1
99	Curing and striking of formwork to suspended slab, Second Floor	1 day	05 May 2027	05 May 2027	98SS+1
100	Balustrades and handrails to stairs, Second Floor	9 days	06 May 2027	15 May 2027	94, 99
101	**WHOLE BUILDING**	**37 days**	**25 Mar 2027**	**10 May 2027**	
102	Formwork to columns and beams	4 days	25 Mar 2027	31 Mar 2027	34
103	Reinforcement to columns and beams	2 days	25 Mar 2027	27 Mar 2027	34
104	Inspection and approval of reinforcement	2 days	27 Mar 2027	30 Mar 2027	103SS+1
105	Formwork to staircase	4 days	06 May 2027	10 May 2027	94, 99
106	Reinforcement to staircase	2 days	06 May 2027	07 May 2027	94, 99
107	Inspection and approval of reinforcement	2 days	07 May 2027	08 May 2027	106SS+1
108	**ROOF**	**3 days**	**21 Aug 2027**	**24 Aug 2027**	

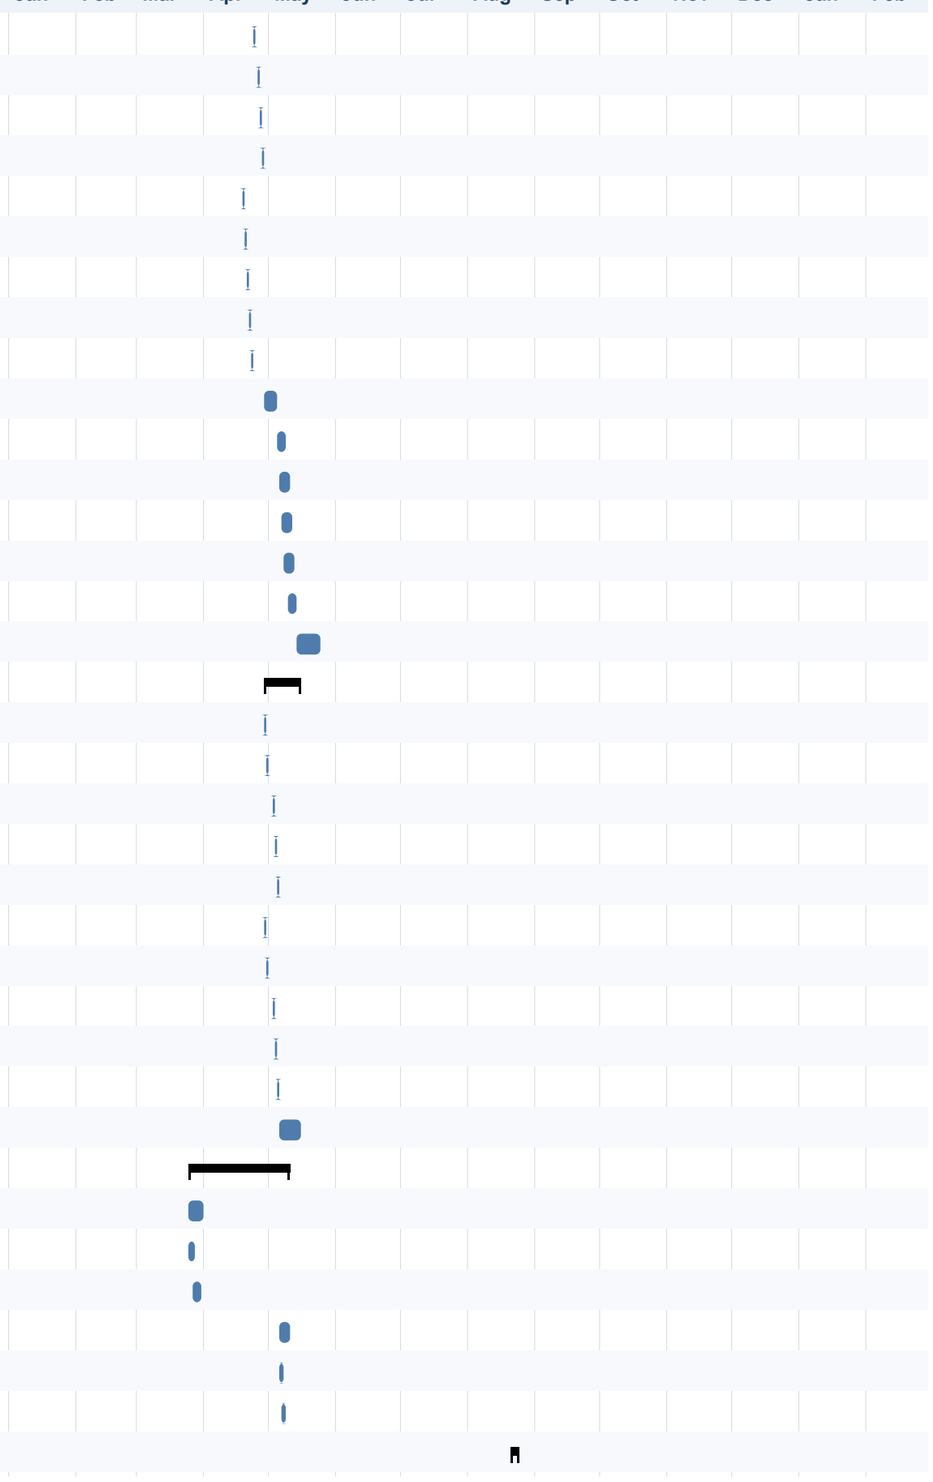


PROGRAMME OF WORKS: IKEJA CORPORATE OFFICE

Demo Partners QS Contract period: 11 January 2027 to 29 February 2028 (14 months) Monday to Saturday, Nigerian public holidays excluded Revision B, 02 November 2026

Critical With float

ID	Task Name	Duration	Start	Finish	Predecessors
109	Roof decking	2 days	21 Aug 2027	23 Aug 2027	17, 139, 94, 137
110	Roof insulation	2 days	23 Aug 2027	24 Aug 2027	109SS+1
111	**WALLS AND PARTITIONS**	**105 days**	**19 Apr 2027**	**20 Aug 2027**	
112	**GROUND FLOOR**	**30 days**	**19 Apr 2027**	**24 May 2027**	
113	Setting out and first lift of walling, Ground Floor, zone A	6 days	19 Apr 2027	24 Apr 2027	59
114	Setting out and first lift of walling, Ground Floor, zone B	6 days	21 Apr 2027	27 Apr 2027	113SS+2
115	Blockwork and brickwork to full height, Ground Floor, zone A	6 days	23 Apr 2027	29 Apr 2027	114SS+2
116	Blockwork and brickwork to full height, Ground Floor, zone B	6 days	26 Apr 2027	03 May 2027	115SS+2
117	Lintels, stiffeners and wall plates, Ground Floor, zone A	6 days	28 Apr 2027	05 May 2027	116SS+2
118	Lintels, stiffeners and wall plates, Ground Floor, zone B	6 days	30 Apr 2027	07 May 2027	117SS+2
119	Head and base tracks, Ground Floor, zone A	11 days	19 Apr 2027	30 Apr 2027	59
120	Head and base tracks, Ground Floor, zone B	11 days	24 Apr 2027	07 May 2027	119SS+5
121	Stud framing to walls and partitions, Ground Floor, zone A	11 days	30 Apr 2027	13 May 2027	120SS+5
122	Stud framing to walls and partitions, Ground Floor, zone B	11 days	07 May 2027	19 May 2027	121SS+5
123	Walls	4 days	20 May 2027	24 May 2027	118, 122
124	**FIRST FLOOR**	**35 days**	**25 May 2027**	**05 Jul 2027**	
125	Head and base tracks, First Floor, zone A	14 days	25 May 2027	09 Jun 2027	81, 76, 123
126	Head and base tracks, First Floor, zone B	14 days	02 Jun 2027	18 Jun 2027	125SS+7
127	Stud framing to walls and partitions, First Floor, zone A	14 days	10 Jun 2027	26 Jun 2027	126SS+7
128	Stud framing to walls and partitions, First Floor, zone B	14 days	19 Jun 2027	05 Jul 2027	127SS+7
129	**SECOND FLOOR**	**31 days**	**06 Jul 2027**	**10 Aug 2027**	
130	Head and base tracks, Second Floor, zone A	13 days	06 Jul 2027	20 Jul 2027	94, 99, 128
131	Head and base tracks, Second Floor, zone B	13 days	13 Jul 2027	27 Jul 2027	130SS+6
132	Stud framing to walls and partitions, Second Floor, zone A	13 days	20 Jul 2027	03 Aug 2027	131SS+6
133	Stud framing to walls and partitions, Second Floor, zone B	13 days	27 Jul 2027	10 Aug 2027	132SS+6
134	**ROOF**	**9 days**	**11 Aug 2027**	**20 Aug 2027**	
135	Setting out and first lift of walling, Roof	5 days	11 Aug 2027	16 Aug 2027	94, 99, 133
136	Blockwork and brickwork to full height, Roof	5 days	13 Aug 2027	18 Aug 2027	135SS+2
137	Lintels, stiffeners and wall plates, Roof	5 days	16 Aug 2027	20 Aug 2027	136SS+2
138	Head and base tracks, Roof	6 days	11 Aug 2027	17 Aug 2027	94, 99, 133
139	Stud framing to walls and partitions, Roof	6 days	13 Aug 2027	19 Aug 2027	138SS+2
140	**WINDOWS AND DOORS**	**142 days**	**25 May 2027**	**08 Nov 2027**	
141	**GROUND FLOOR**	**142 days**	**25 May 2027**	**08 Nov 2027**	
142	Window frames and subframes, Ground Floor, zone A	58 days	25 May 2027	31 Jul 2027	20, 123
143	Window frames and subframes, Ground Floor, zone B	58 days	28 Jun 2027	02 Sep 2027	142SS+28
144	Glazing and sealing of windows, Ground Floor, zone A	58 days	30 Jul 2027	06 Oct 2027	143SS+28

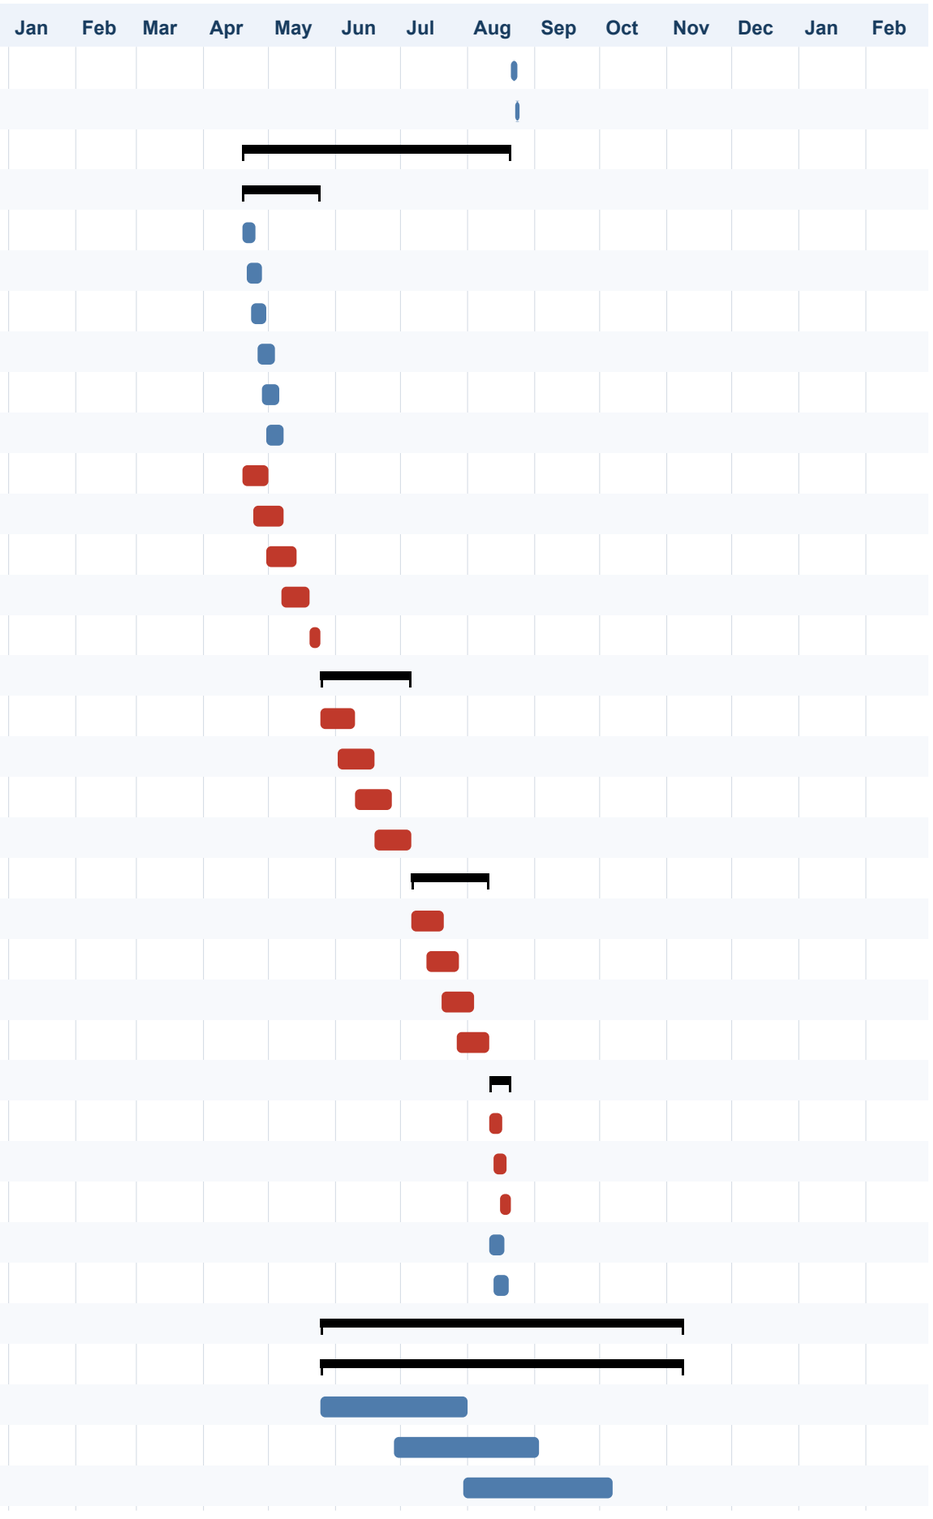


PROGRAMME OF WORKS: IKEJA CORPORATE OFFICE

Demo Partners QS Contract period: 11 January 2027 to 29 February 2028 (14 months) Monday to Saturday, Nigerian public holidays excluded Revision B, 02 November 2026

Critical With float

ID	Task Name	Duration	Start	Finish	Predecessors
145	Glazing and sealing of windows, Ground Floor, zone B	58 days	01 Sep 2027	08 Nov 2027	144SS+28
146	Door frames and linings, Ground Floor, zone A	5 days	25 May 2027	29 May 2027	22, 123
147	Door frames and linings, Ground Floor, zone B	5 days	27 May 2027	01 Jun 2027	146SS+2
148	Hanging of doors and ironmongery, Ground Floor, zone A	5 days	29 May 2027	03 Jun 2027	147SS+2
149	Hanging of doors and ironmongery, Ground Floor, zone B	5 days	01 Jun 2027	05 Jun 2027	148SS+2
150	**FIRST FLOOR**	**11 days**	**06 Jul 2027**	**17 Jul 2027**	
151	Window frames and subframes, First Floor	7 days	06 Jul 2027	13 Jul 2027	128
152	Glazing and sealing of windows, First Floor	7 days	10 Jul 2027	17 Jul 2027	151SS+4
153	Door frames and linings, First Floor, zone A	5 days	06 Jul 2027	10 Jul 2027	128
154	Door frames and linings, First Floor, zone B	5 days	08 Jul 2027	13 Jul 2027	153SS+2
155	Hanging of doors and ironmongery, First Floor, zone A	5 days	10 Jul 2027	15 Jul 2027	154SS+2
156	Hanging of doors and ironmongery, First Floor, zone B	5 days	13 Jul 2027	17 Jul 2027	155SS+2
157	**SECOND FLOOR**	**11 days**	**11 Aug 2027**	**23 Aug 2027**	
158	Window frames and subframes, Second Floor, zone A	5 days	11 Aug 2027	16 Aug 2027	133
159	Window frames and subframes, Second Floor, zone B	5 days	13 Aug 2027	18 Aug 2027	158SS+2
160	Glazing and sealing of windows, Second Floor, zone A	5 days	16 Aug 2027	20 Aug 2027	159SS+2
161	Glazing and sealing of windows, Second Floor, zone B	5 days	18 Aug 2027	23 Aug 2027	160SS+2
162	Door frames and linings, Second Floor	7 days	11 Aug 2027	18 Aug 2027	133
163	Hanging of doors and ironmongery, Second Floor	7 days	16 Aug 2027	23 Aug 2027	162SS+4
164	**PARAPET**	**11 days**	**21 Aug 2027**	**02 Sep 2027**	
165	Window frames and subframes, Parapet	7 days	21 Aug 2027	28 Aug 2027	139, 137
166	Glazing and sealing of windows, Parapet	7 days	26 Aug 2027	02 Sep 2027	165SS+4
167	**FINISHES**	**127 days**	**03 Sep 2027**	**01 Feb 2028**	
168	**GROUND FLOOR**	**11 days**	**07 Sep 2027**	**18 Sep 2027**	
169	Ceiling boards and tiles, Ground Floor	7 days	07 Sep 2027	14 Sep 2027	24, 180, 110, 123
170	Access panels and trims, Ground Floor	7 days	11 Sep 2027	18 Sep 2027	169SS+4
171	**FIRST FLOOR**	**11 days**	**07 Sep 2027**	**18 Sep 2027**	
172	Ceiling boards and tiles, First Floor	7 days	07 Sep 2027	14 Sep 2027	180, 110, 128
173	Access panels and trims, First Floor	7 days	11 Sep 2027	18 Sep 2027	172SS+4
174	**SECOND FLOOR**	**11 days**	**07 Sep 2027**	**18 Sep 2027**	
175	Ceiling boards and tiles, Second Floor	7 days	07 Sep 2027	14 Sep 2027	180, 110, 133
176	Access panels and trims, Second Floor	7 days	11 Sep 2027	18 Sep 2027	175SS+4
177	**WHOLE BUILDING**	**127 days**	**03 Sep 2027**	**01 Feb 2028**	
178	Floor screeding	4 days	24 Jan 2028	27 Jan 2028	139, 176, 137, 110, 184
179	Internal plastering	2 days	03 Sep 2027	04 Sep 2027	139, 166, 137, 110
180	External rendering	2 days	04 Sep 2027	06 Sep 2027	179SS+1

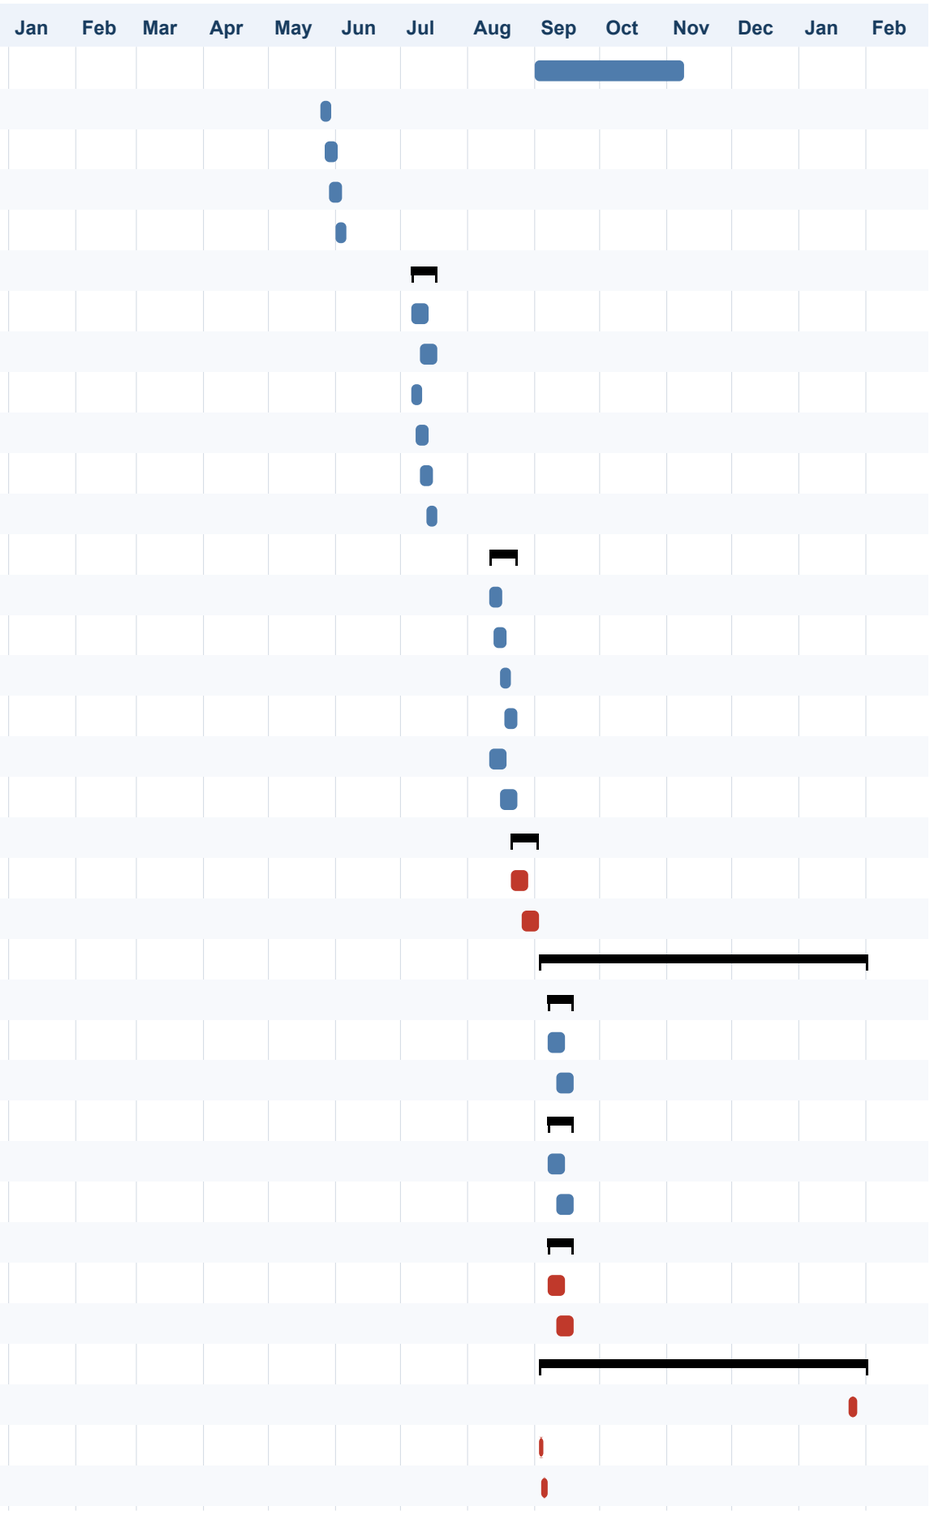

PROGRAMME OF WORKS: IKEJA CORPORATE OFFICE

Demo Partners QS Contract period: 11 January 2027 to 29 February 2028 (14 months) Monday to Saturday, Nigerian public holidays excluded Revision B, 02 November 2026

Critical With float

ID	Task Name	Duration	Start	Finish	Predecessors
181	Mist coat and first coat of paint, zone A	42 days	20 Sep 2027	08 Nov 2027	139, 176, 180, 137, 110
182	Mist coat and first coat of paint, zone B	42 days	15 Oct 2027	02 Dec 2027	181SS+21
183	Final coats of paint and touch-up, zone A	42 days	09 Nov 2027	28 Dec 2027	182SS+21
184	Final coats of paint and touch-up, zone B	42 days	03 Dec 2027	22 Jan 2028	183SS+21
185	Fittings and fixtures	4 days	28 Jan 2028	01 Feb 2028	139, 178, 137, 163, 110
186	**M&E SERVICES**	**73 days**	**26 Apr 2027**	**21 Jul 2027**	
187	**SECOND FLOOR**	**8 days**	**13 Jul 2027**	**21 Jul 2027**	
188	Electrical first fix: conduits, sleeves and pipework, Second Floor	6 days	13 Jul 2027	19 Jul 2027	130SS+6
189	Electrical first fix: cabling and draw wires, Second Floor	6 days	15 Jul 2027	21 Jul 2027	188SS+2
190	**WHOLE BUILDING**	**11 days**	**26 Apr 2027**	**08 May 2027**	
191	Electrical first fix: conduits, sleeves and pipework, zone A	5 days	26 Apr 2027	30 Apr 2027	26, 113SS+6, 119SS+6
192	Electrical first fix: conduits, sleeves and pipework, zone B	5 days	28 Apr 2027	04 May 2027	191SS+2
193	Electrical first fix: cabling and draw wires, zone A	5 days	30 Apr 2027	06 May 2027	192SS+2
194	Electrical first fix: cabling and draw wires, zone B	5 days	04 May 2027	08 May 2027	193SS+2
195	**EXTERNAL WORKS**	**4 days**	**25 Aug 2027**	**28 Aug 2027**	
196	External works (whole building)	4 days	25 Aug 2027	28 Aug 2027	110
197	**TESTING, COMMISSIONING AND HANDOVER**	**188 days**	**22 Jul 2027**	**29 Feb 2028**	
198	Electrical installation testing and certification	8 days	22 Jul 2027	30 Jul 2027	189, 194
199	Snagging and rectification, Ground Floor	4 days	02 Feb 2028	05 Feb 2028	161, 66, 198, 145, 88, 185, 156, 149, 105, 170, 173, 104, 102, 196, 107, 100, 152
200	Snagging and rectification, First Floor	4 days	04 Feb 2028	08 Feb 2028	199SS+2
201	Snagging and rectification, Second Floor	4 days	07 Feb 2028	10 Feb 2028	200SS+2
202	Snagging and rectification, Roof	4 days	09 Feb 2028	12 Feb 2028	201SS+2
203	Snagging and rectification, Parapet	4 days	11 Feb 2028	15 Feb 2028	202SS+2
204	Final builders clean	5 days	16 Feb 2028	21 Feb 2028	203
205	O&M manuals, as-built drawings and handover documents	5 days	22 Feb 2028	26 Feb 2028	204
206	Client inspection and handover	2 days	28 Feb 2028	29 Feb 2028	205
207	**Practical completion**	**0 days**	**29 Feb 2028**	**29 Feb 2028**	**206**

