
PROGRAMME OF WORKS: IKOYI DUPLEX

Demo Partners QS Contract period: 01 February 2027 to 30 July 2027 (6 months) Monday to Saturday, Nigerian public holidays excluded Revision B, 02 November 2026

Critical With float

ID	Task Name	Duration	Start	Finish	Predecessors
1	**PROGRAMME OF WORKS**	**146 days**	**01 Feb 2027**	**24 Jul 2027**	
2	**KEY DATES**	**1 day**	**01 Feb 2027**	**01 Feb 2027**	
3	**Letter of award**	**0 days**	**01 Feb 2027**	**01 Feb 2027**	
4	**Site possession and handover of site**	**0 days**	**01 Feb 2027**	**01 Feb 2027**	**3**
5	**PRELIMINARIES AND MOBILISATION**	**20 days**	**01 Feb 2027**	**23 Feb 2027**	
6	Mobilisation of personnel and equipment	10 days	01 Feb 2027	11 Feb 2027	4
7	Site clearance	6 days	03 Feb 2027	09 Feb 2027	6SS+2
8	Hoarding, gates and site security	8 days	05 Feb 2027	13 Feb 2027	7SS+2
9	Site offices, stores and welfare facilities	10 days	08 Feb 2027	18 Feb 2027	8SS+2
10	Temporary water and power supply	5 days	12 Feb 2027	17 Feb 2027	9SS+4
11	Setting out and survey of building lines	4 days	18 Feb 2027	22 Feb 2027	10
12	Approval of setting out by the consultant	1 day	23 Feb 2027	23 Feb 2027	11
13	**PROCUREMENT**	**45 days**	**01 Feb 2027**	**24 Mar 2027**	
14	Roofing materials: samples and approval	5 days	01 Feb 2027	05 Feb 2027	4
15	Roofing materials: delivery to site	15 days	06 Feb 2027	23 Feb 2027	14
16	Windows and glazing: shop drawings	10 days	01 Feb 2027	11 Feb 2027	4
17	Windows and glazing: consultant approval	5 days	12 Feb 2027	17 Feb 2027	16
18	Windows and glazing: manufacture and delivery	30 days	18 Feb 2027	24 Mar 2027	17
19	Doors and ironmongery: schedule approval	5 days	01 Feb 2027	05 Feb 2027	4
20	Doors and ironmongery: manufacture and delivery	25 days	06 Feb 2027	06 Mar 2027	19
21	Ceiling materials: samples and approval	5 days	01 Feb 2027	05 Feb 2027	4
22	Ceiling materials: delivery to site	15 days	06 Feb 2027	23 Feb 2027	21
23	**SUBSTRUCTURE**	**30 days**	**24 Feb 2027**	**01 Apr 2027**	
24	**FOUNDATION**	**21 days**	**24 Feb 2027**	**19 Mar 2027**	
25	Formwork to foundations and ground slab, Foundation	12 days	24 Feb 2027	09 Mar 2027	12
26	Reinforcement to foundations and ground slab, Foundation	4 days	10 Mar 2027	13 Mar 2027	25
27	Formwork to foundations and ground slab, Foundation	4 days	11 Mar 2027	15 Mar 2027	26SS+1
28	Inspection and approval of reinforcement, Foundation	4 days	12 Mar 2027	16 Mar 2027	27SS+1
29	Concrete placement to foundations and ground slab, Foundation	4 days	13 Mar 2027	17 Mar 2027	28SS+1
30	Curing and striking of formwork to foundations and ground slab, Foundation	4 days	15 Mar 2027	18 Mar 2027	29SS+1
31	Anti-termite treatment and damp-proof membrane, Foundation	1 day	19 Mar 2027	19 Mar 2027	30
32	**GROUND FLOOR**	**9 days**	**20 Mar 2027**	**01 Apr 2027**	
33	Formwork to foundations and ground slab, Ground Floor	1 day	20 Mar 2027	20 Mar 2027	31
34	Reinforcement to foundations and ground slab, Ground Floor	1 day	22 Mar 2027	22 Mar 2027	33
35	Formwork to foundations and ground slab, Ground Floor	1 day	23 Mar 2027	23 Mar 2027	34SS+1
36	Inspection and approval of reinforcement, Ground Floor	1 day	24 Mar 2027	24 Mar 2027	35SS+1

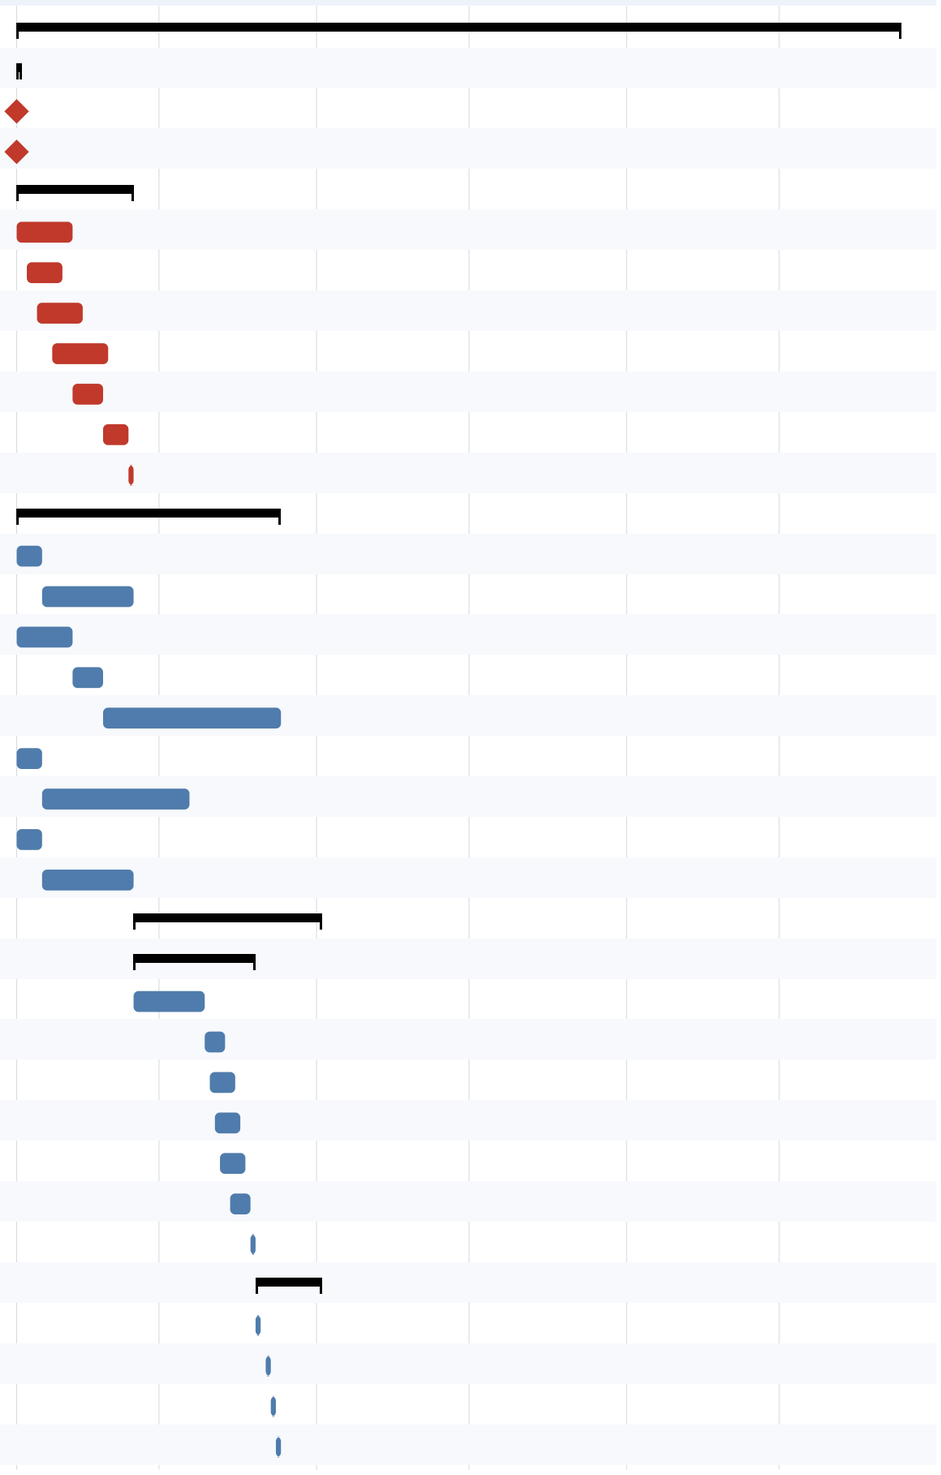


PROGRAMME OF WORKS: IKOYI DUPLEX

Demo Partners QS Contract period: 01 February 2027 to 30 July 2027 (6 months) Monday to Saturday, Nigerian public holidays excluded Revision B, 02 November 2026

Critical With float

ID	Task Name	Duration	Start	Finish	Predecessors
37	Concrete placement to foundations and ground slab, Ground Floor	1 day	25 Mar 2027	25 Mar 2027	36SS+1
38	Curing and striking of formwork to foundations and ground slab, Ground F...	1 day	27 Mar 2027	27 Mar 2027	37SS+1
39	Anti-termite treatment and damp-proof membrane, Ground Floor	3 days	30 Mar 2027	01 Apr 2027	38
40	**SUPERSTRUCTURE**	**18 days**	**24 Feb 2027**	**16 Mar 2027**	
41	**GROUND FLOOR**	**18 days**	**24 Feb 2027**	**16 Mar 2027**	
42	Steel stair stringers and treads, Ground Floor	4 days	24 Feb 2027	27 Feb 2027	12
43	Balustrades and handrails to stairs, Ground Floor	10 days	01 Mar 2027	11 Mar 2027	42
44	Stairs	4 days	12 Mar 2027	16 Mar 2027	43
45	**FIRST FLOOR**	**12 days**	**24 Feb 2027**	**09 Mar 2027**	
46	Suspended floor construction, First Floor	12 days	24 Feb 2027	09 Mar 2027	12
47	**ROOF**	**9 days**	**29 May 2027**	**08 Jun 2027**	
48	Roof structure and purlins	9 days	29 May 2027	08 Jun 2027	15, 89
49	**WALLS AND PARTITIONS**	**78 days**	**24 Feb 2027**	**28 May 2027**	
50	**GROUND FLOOR**	**31 days**	**24 Feb 2027**	**02 Apr 2027**	
51	Setting out and first lift of walling, Ground Floor, zone A	4 days	24 Feb 2027	27 Feb 2027	12
52	Setting out and first lift of walling, Ground Floor, zone B	4 days	25 Feb 2027	01 Mar 2027	51SS+1
53	Blockwork and brickwork to full height, Ground Floor, zone A	4 days	26 Feb 2027	02 Mar 2027	52SS+1
54	Blockwork and brickwork to full height, Ground Floor, zone B	4 days	27 Feb 2027	03 Mar 2027	53SS+1
55	Lintels, stiffeners and wall plates, Ground Floor, zone A	4 days	01 Mar 2027	04 Mar 2027	54SS+1
56	Lintels, stiffeners and wall plates, Ground Floor, zone B	4 days	02 Mar 2027	05 Mar 2027	55SS+1
57	Head and base tracks, Ground Floor, zone A	6 days	24 Feb 2027	02 Mar 2027	12
58	Head and base tracks, Ground Floor, zone B	6 days	27 Feb 2027	05 Mar 2027	57SS+3
59	Stud framing to walls and partitions, Ground Floor, zone A	6 days	03 Mar 2027	09 Mar 2027	58SS+3
60	Stud framing to walls and partitions, Ground Floor, zone B	6 days	06 Mar 2027	12 Mar 2027	59SS+3
61	Boarding to first side, Ground Floor	6 days	13 Mar 2027	19 Mar 2027	56, 60
62	Insulation and boarding to second side, Ground Floor	6 days	17 Mar 2027	23 Mar 2027	61SS+3
63	Taping and jointing, Ground Floor	6 days	20 Mar 2027	27 Mar 2027	62SS+3
64	Walls	4 days	30 Mar 2027	02 Apr 2027	63
65	**FIRST FLOOR**	**31 days**	**03 Apr 2027**	**10 May 2027**	
66	Setting out and first lift of walling, First Floor, zone A	4 days	03 Apr 2027	07 Apr 2027	46, 64
67	Setting out and first lift of walling, First Floor, zone B	4 days	05 Apr 2027	08 Apr 2027	66SS+1
68	Blockwork and brickwork to full height, First Floor, zone A	4 days	06 Apr 2027	09 Apr 2027	67SS+1
69	Blockwork and brickwork to full height, First Floor, zone B	4 days	07 Apr 2027	10 Apr 2027	68SS+1
70	Lintels, stiffeners and wall plates, First Floor, zone A	4 days	08 Apr 2027	12 Apr 2027	69SS+1
71	Lintels, stiffeners and wall plates, First Floor, zone B	4 days	09 Apr 2027	13 Apr 2027	70SS+1
72	Head and base tracks, First Floor, zone A	6 days	03 Apr 2027	09 Apr 2027	46, 64

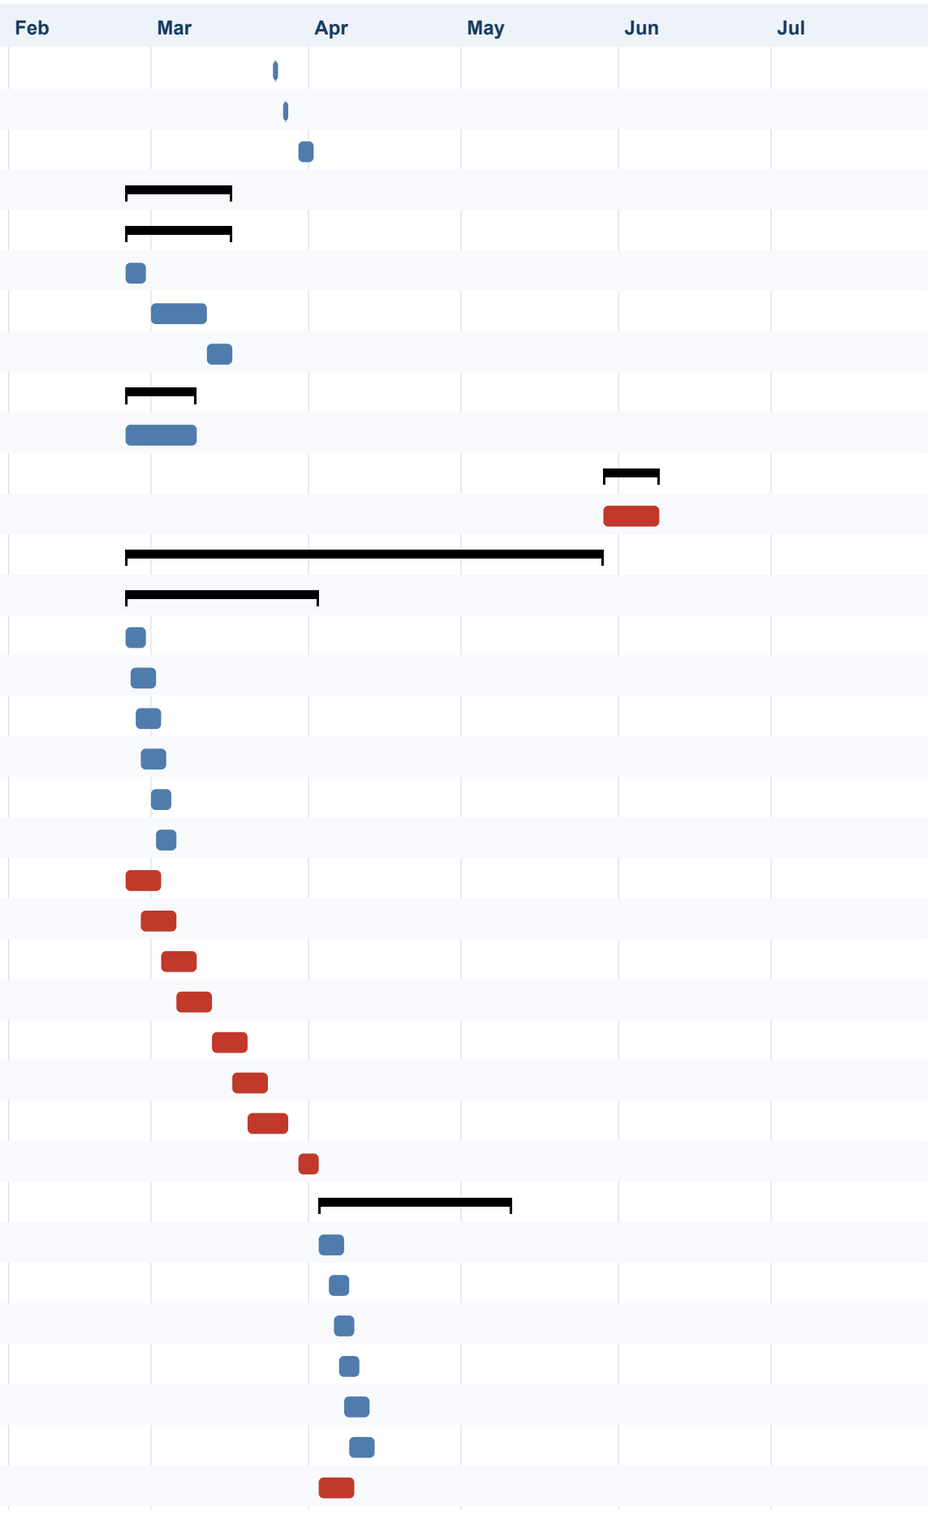


PROGRAMME OF WORKS: IKOYI DUPLEX

Demo Partners QS Contract period: 01 February 2027 to 30 July 2027 (6 months) Monday to Saturday, Nigerian public holidays excluded Revision B, 02 November 2026

Critical With float

ID	Task Name	Duration	Start	Finish	Predecessors
73	Head and base tracks, First Floor, zone B	6 days	07 Apr 2027	13 Apr 2027	72SS+3
74	Stud framing to walls and partitions, First Floor, zone A	6 days	10 Apr 2027	16 Apr 2027	73SS+3
75	Stud framing to walls and partitions, First Floor, zone B	6 days	14 Apr 2027	20 Apr 2027	74SS+3
76	Boarding to first side, First Floor	6 days	21 Apr 2027	27 Apr 2027	71, 75
77	Insulation and boarding to second side, First Floor	6 days	24 Apr 2027	30 Apr 2027	76SS+3
78	Taping and jointing, First Floor	6 days	28 Apr 2027	05 May 2027	77SS+3
79	Walls	4 days	06 May 2027	10 May 2027	78
80	**ROOF**	**16 days**	**11 May 2027**	**28 May 2027**	
81	Setting out and first lift of walling, Roof	6 days	11 May 2027	17 May 2027	46, 79
82	Blockwork and brickwork to full height, Roof	6 days	14 May 2027	20 May 2027	81SS+3
83	Lintels, stiffeners and wall plates, Roof	6 days	18 May 2027	24 May 2027	82SS+3
84	Head and base tracks, Roof	1 day	11 May 2027	11 May 2027	46, 79
85	Stud framing to walls and partitions, Roof	1 day	12 May 2027	12 May 2027	84SS+1
86	Boarding to first side, Roof	1 day	25 May 2027	25 May 2027	83, 85
87	Insulation and boarding to second side, Roof	1 day	26 May 2027	26 May 2027	86SS+1
88	Taping and jointing, Roof	1 day	27 May 2027	27 May 2027	87SS+1
89	Walls	1 day	28 May 2027	28 May 2027	88
90	**WINDOWS AND DOORS**	**49 days**	**03 Apr 2027**	**31 May 2027**	
91	**GROUND FLOOR**	**9 days**	**03 Apr 2027**	**13 Apr 2027**	
92	Window frames and subframes, Ground Floor	4 days	03 Apr 2027	07 Apr 2027	18, 64
93	Glazing and sealing of windows, Ground Floor	4 days	05 Apr 2027	08 Apr 2027	92SS+1
94	Door frames and linings, Ground Floor	6 days	03 Apr 2027	09 Apr 2027	20, 64
95	Hanging of doors and ironmongery, Ground Floor	6 days	07 Apr 2027	13 Apr 2027	94SS+3
96	**FIRST FLOOR**	**13 days**	**11 May 2027**	**25 May 2027**	
97	Window frames and subframes, First Floor	9 days	11 May 2027	20 May 2027	79
98	Glazing and sealing of windows, First Floor	9 days	15 May 2027	25 May 2027	97SS+4
99	Door frames and linings, First Floor	9 days	11 May 2027	20 May 2027	79
100	Hanging of doors and ironmongery, First Floor	9 days	15 May 2027	25 May 2027	99SS+4
101	**ROOF**	**2 days**	**29 May 2027**	**31 May 2027**	
102	Window frames and subframes, Roof	1 day	29 May 2027	29 May 2027	89
103	Glazing and sealing of windows, Roof	1 day	31 May 2027	31 May 2027	102SS+1
104	**FINISHES**	**19 days**	**09 Jun 2027**	**01 Jul 2027**	
105	**GROUND FLOOR**	**19 days**	**09 Jun 2027**	**01 Jul 2027**	
106	Floor tiling, Ground Floor	3 days	23 Jun 2027	25 Jun 2027	111, 64, 48
107	Grouting and skirtings, Ground Floor	3 days	24 Jun 2027	26 Jun 2027	106SS+1
108	Floor coverings and underlay, Ground Floor	4 days	28 Jun 2027	01 Jul 2027	107

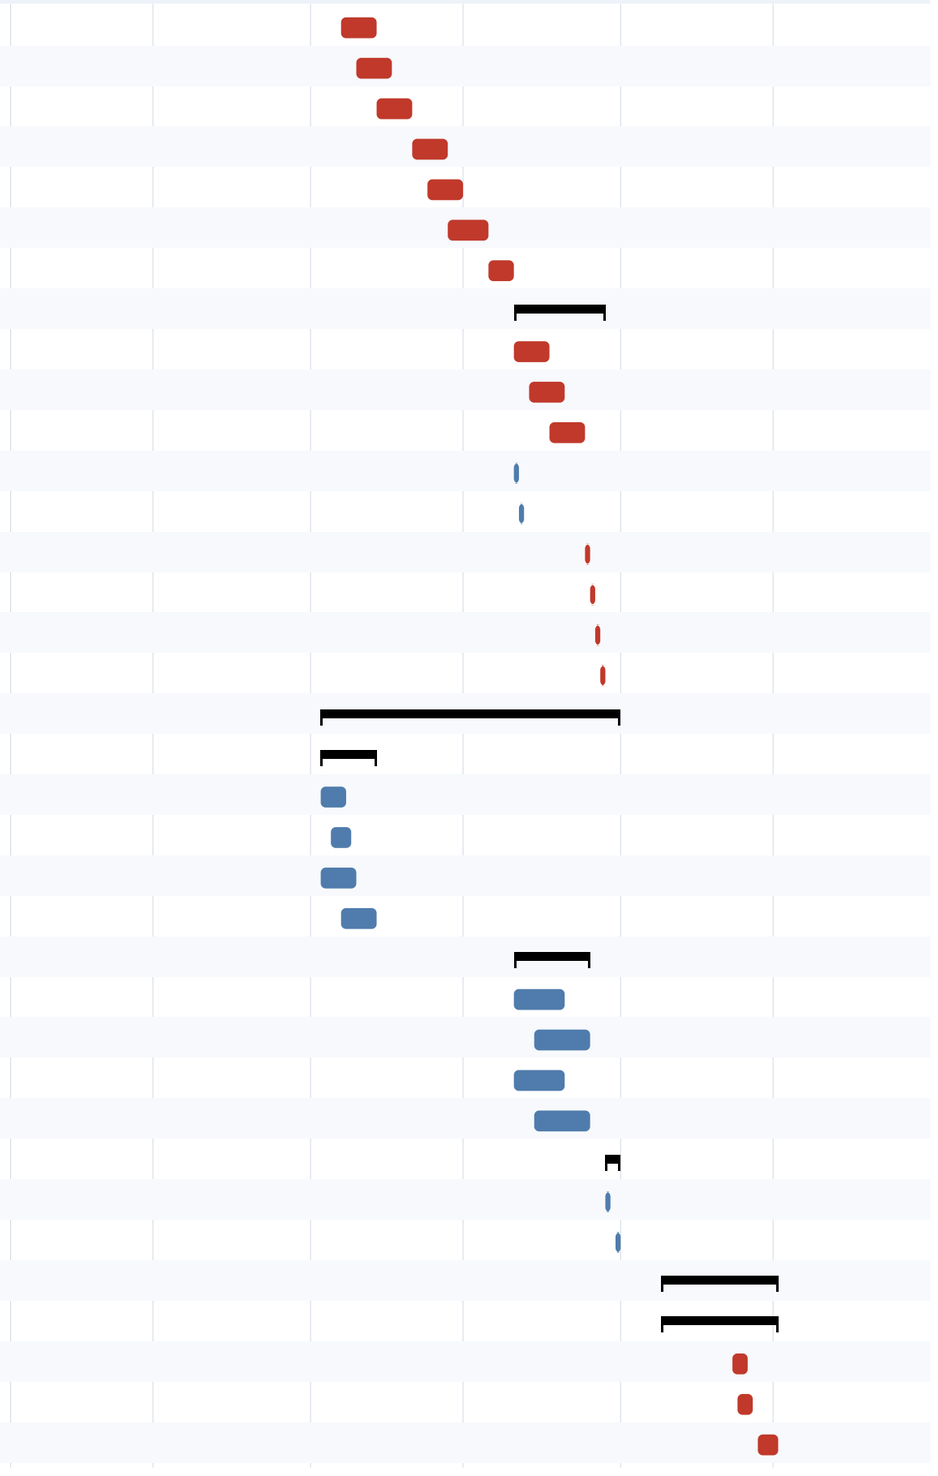

PROGRAMME OF WORKS: IKOYI DUPLEX

Demo Partners QS Contract period: 01 February 2027 to 30 July 2027 (6 months) Monday to Saturday, Nigerian public holidays excluded Revision B, 02 November 2026

Critical With float

ID	Task Name	Duration	Start	Finish	Predecessors
109	Ceiling suspension grid, Ground Floor	7 days	09 Jun 2027	17 Jun 2027	22, 64, 48
110	Ceiling boards and tiles, Ground Floor	3 days	18 Jun 2027	21 Jun 2027	109
111	Access panels and trims, Ground Floor	3 days	19 Jun 2027	22 Jun 2027	110SS+1
112	**FIRST FLOOR**	**19 days**	**09 Jun 2027**	**01 Jul 2027**	
113	Floor tiling, First Floor	3 days	23 Jun 2027	25 Jun 2027	118, 79, 48
114	Grouting and skirtings, First Floor	3 days	24 Jun 2027	26 Jun 2027	113SS+1
115	Floor coverings and underlay, First Floor	4 days	28 Jun 2027	01 Jul 2027	114
116	Ceiling suspension grid, First Floor	7 days	09 Jun 2027	17 Jun 2027	79, 48
117	Ceiling boards and tiles, First Floor	3 days	18 Jun 2027	21 Jun 2027	116
118	Access panels and trims, First Floor	3 days	19 Jun 2027	22 Jun 2027	117SS+1
119	**EXTERNAL WORKS**	**10 days**	**09 Jun 2027**	**21 Jun 2027**	
120	External works: paving, kerbs and landscaping	10 days	09 Jun 2027	21 Jun 2027	48
121	**TESTING, COMMISSIONING AND HANDOVER**	**20 days**	**02 Jul 2027**	**24 Jul 2027**	
122	Snagging and rectification, Ground Floor	4 days	02 Jul 2027	06 Jul 2027	39, 44, 93, 98, 103, 95, 100, 108, 115, 120
123	Snagging and rectification, First Floor	4 days	05 Jul 2027	08 Jul 2027	122SS+2
124	Snagging and rectification, Roof	4 days	07 Jul 2027	10 Jul 2027	123SS+2
125	Final builders clean	5 days	12 Jul 2027	16 Jul 2027	124
126	O&M manuals, as-built drawings and handover documents	5 days	17 Jul 2027	22 Jul 2027	125
127	Client inspection and handover	2 days	23 Jul 2027	24 Jul 2027	126
128	**Practical completion**	**0 days**	**24 Jul 2027**	**24 Jul 2027**	**127**

