
# PROGRAMME OF WORKS: LEKKI OFFICE BLOCK



Demo Partners QS  Contract period: 01 December 2026 to 30 September 2027 (10 months)  Monday to Saturday, Nigerian public holidays excluded  Revision B, 02 November 2026

Critical  With float

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| **1** | **PROGRAMME OF WORKS** | **239 days** | **01 Dec 2026** | **13 Sep 2027** | |
| **2** | **KEY DATES** | **1 day** | **01 Dec 2026** | **01 Dec 2026** | |
| **3** | **Letter of award** | **0 days** | **01 Dec 2026** | **01 Dec 2026** | |
| **4** | **Site possession and handover of site** | **0 days** | **01 Dec 2026** | **01 Dec 2026** | **3** |
| **5** | **PRELIMINARIES AND MOBILISATION** | **20 days** | **01 Dec 2026** | **23 Dec 2026** | |
| 6 | Mobilisation of personnel and equipment | 10 days | 01 Dec 2026 | 11 Dec 2026 | 4 |
| 7 | Site clearance | 6 days | 03 Dec 2026 | 09 Dec 2026 | 6SS+2 |
| 8 | Hoarding, gates and site security | 8 days | 05 Dec 2026 | 14 Dec 2026 | 7SS+2 |
| 9 | Site offices, stores and welfare facilities | 10 days | 08 Dec 2026 | 18 Dec 2026 | 8SS+2 |
| 10 | Temporary water and power supply | 5 days | 12 Dec 2026 | 17 Dec 2026 | 9SS+4 |
| 11 | Setting out and survey of building lines | 4 days | 18 Dec 2026 | 22 Dec 2026 | 10 |
| 12 | Approval of setting out by the consultant | 1 day | 23 Dec 2026 | 23 Dec 2026 | 11 |
| **13** | **PROCUREMENT** | **70 days** | **01 Dec 2026** | **23 Feb 2027** | |
| 14 | Structural steel: shop drawings | 10 days | 01 Dec 2026 | 11 Dec 2026 | 4 |
| 15 | Structural steel: consultant approval | 5 days | 12 Dec 2026 | 17 Dec 2026 | 14 |
| 16 | Roofing materials: samples and approval | 5 days | 01 Dec 2026 | 05 Dec 2026 | 4 |
| 17 | Roofing materials: delivery to site | 15 days | 07 Dec 2026 | 23 Dec 2026 | 16 |
| 18 | Windows and glazing: shop drawings | 10 days | 01 Dec 2026 | 11 Dec 2026 | 4 |
| 19 | Windows and glazing: consultant approval | 5 days | 12 Dec 2026 | 17 Dec 2026 | 18 |
| 20 | Windows and glazing: manufacture and delivery | 30 days | 18 Dec 2026 | 25 Jan 2027 | 19 |
| 21 | Doors and ironmongery: schedule approval | 5 days | 01 Dec 2026 | 05 Dec 2026 | 4 |
| 22 | Doors and ironmongery: manufacture and delivery | 25 days | 07 Dec 2026 | 07 Jan 2027 | 21 |
| 23 | Ceiling materials: samples and approval | 5 days | 01 Dec 2026 | 05 Dec 2026 | 4 |
| 24 | Ceiling materials: delivery to site | 15 days | 07 Dec 2026 | 23 Dec 2026 | 23 |
| 25 | Mechanical plant: submittals and approval | 10 days | 01 Dec 2026 | 11 Dec 2026 | 4 |
| 26 | Mechanical plant: manufacture and delivery | 45 days | 12 Dec 2026 | 05 Feb 2027 | 25 |
| 27 | Electrical boards and fittings: submittals and approval | 10 days | 01 Dec 2026 | 11 Dec 2026 | 4 |
| 28 | Electrical boards and fittings: delivery to site | 30 days | 12 Dec 2026 | 19 Jan 2027 | 27 |
| 29 | Lifts: order and approval of lift drawings | 10 days | 01 Dec 2026 | 11 Dec 2026 | 4 |
| 30 | Lifts: manufacture and shipping | 60 days | 12 Dec 2026 | 23 Feb 2027 | 29 |
| **31** | **SUBSTRUCTURE** | **18 days** | **24 Dec 2026** | **16 Jan 2027** | |
| **32** | **FOUNDATION** | **11 days** | **24 Dec 2026** | **08 Jan 2027** | |
| 33 | Reinforcement to foundations and ground slab, Foundation | 3 days | 24 Dec 2026 | 29 Dec 2026 | 12 |
| 34 | Formwork to foundations and ground slab, Foundation | 3 days | 29 Dec 2026 | 31 Dec 2026 | 33SS+2 |
| 35 | Inspection and approval of reinforcement, Foundation | 3 days | 31 Dec 2026 | 04 Jan 2027 | 34SS+2 |
| 36 | Concrete placement to foundations and ground slab, Foundation | 3 days | 04 Jan 2027 | 06 Jan 2027 | 35SS+2 |

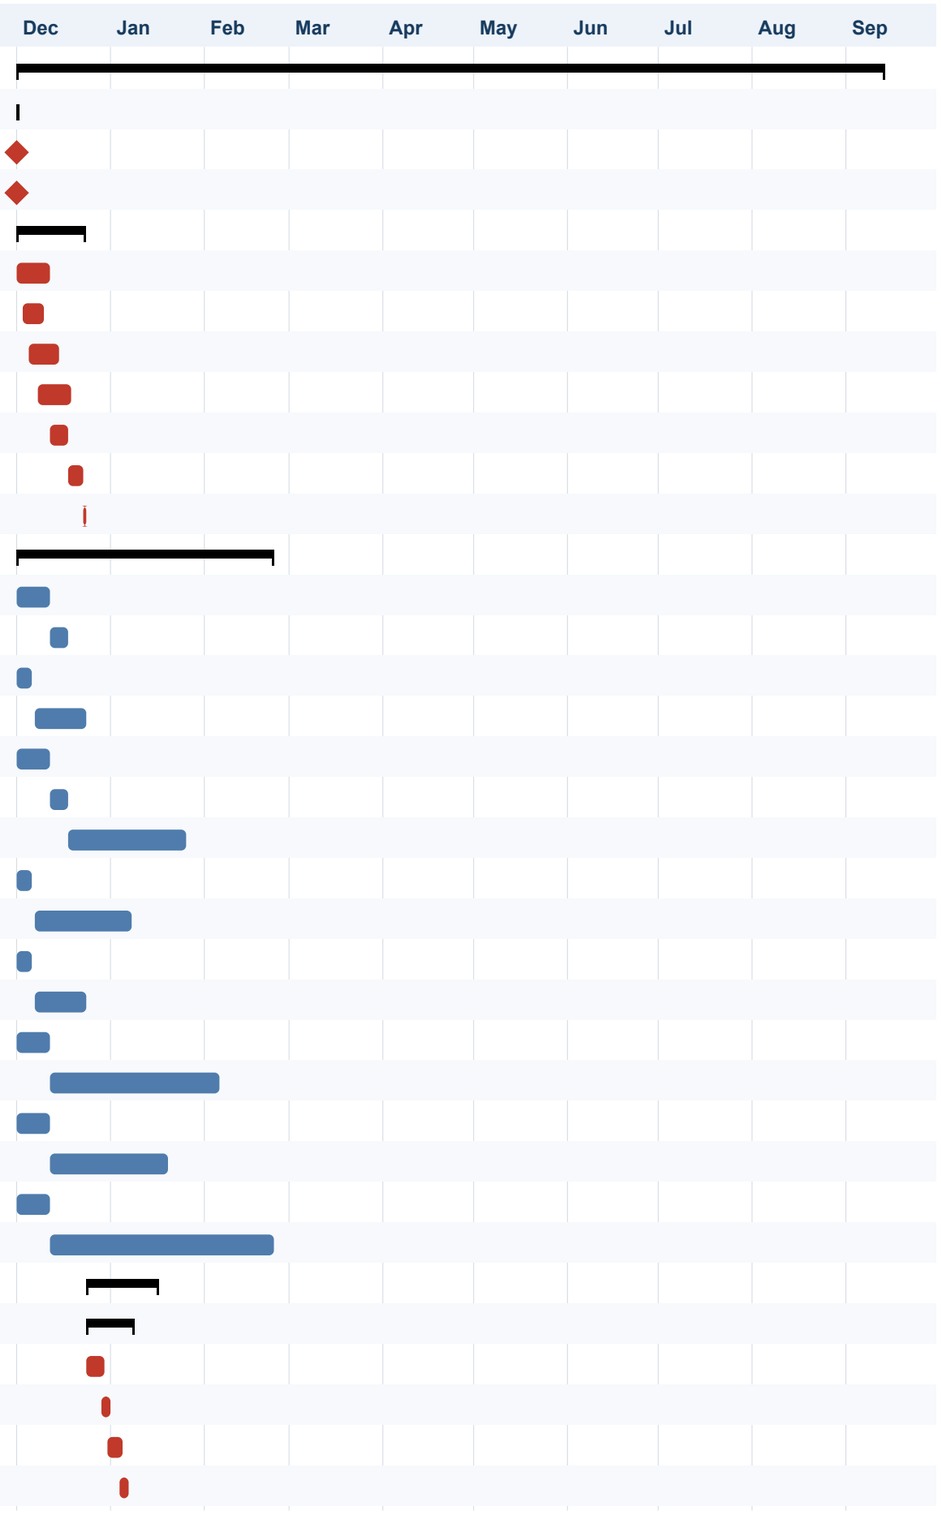


# PROGRAMME OF WORKS: LEKKI OFFICE BLOCK




Demo Partners QS  Contract period: 01 December 2026 to 30 September 2027 (10 months)  Monday to Saturday, Nigerian public holidays excluded  Revision B, 02 November 2026

Critical  With float

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 37 | Curing and striking of formwork to foundations and ground slab, Foundation | 3 days | 06 Jan 2027 | 08 Jan 2027 | 36SS+2 |
| **38** | **GROUND FLOOR** | **7 days** | **09 Jan 2027** | **16 Jan 2027** | |
| 39 | Reinforcement to foundations and ground slab, Ground Floor | 3 days | 09 Jan 2027 | 12 Jan 2027 | 37 |
| 40 | Formwork to foundations and ground slab, Ground Floor | 3 days | 11 Jan 2027 | 13 Jan 2027 | 39SS+1 |
| 41 | Inspection and approval of reinforcement, Ground Floor | 3 days | 12 Jan 2027 | 14 Jan 2027 | 40SS+1 |
| 42 | Concrete placement to foundations and ground slab, Ground Floor | 3 days | 13 Jan 2027 | 15 Jan 2027 | 41SS+1 |
| 43 | Curing and striking of formwork to foundations and ground slab, Ground F... | 3 days | 14 Jan 2027 | 16 Jan 2027 | 42SS+1 |
| **44** | **SUPERSTRUCTURE** | **46 days** | **18 Jan 2027** | **11 Mar 2027** | |
| **45** | **FOUNDATION** | **9 days** | **18 Jan 2027** | **27 Jan 2027** | |
| 46 | Fabrication and delivery of structural steel, Foundation | 3 days | 18 Jan 2027 | 20 Jan 2027 | 15, 43 |
| 47 | Erection of steel columns, Foundation | 3 days | 20 Jan 2027 | 22 Jan 2027 | 46SS+2 |
| 48 | Erection of steel beams and joists, Foundation | 3 days | 22 Jan 2027 | 25 Jan 2027 | 47SS+2 |
| 49 | Bolting, plumbing and final tightening, Foundation | 3 days | 25 Jan 2027 | 27 Jan 2027 | 48SS+2 |
| **50** | **GROUND FLOOR** | **34 days** | **28 Jan 2027** | **08 Mar 2027** | |
| 51 | Fabrication and delivery of structural steel, Ground Floor | 7 days | 28 Jan 2027 | 04 Feb 2027 | 43, 49 |
| 52 | Erection of steel columns, Ground Floor | 7 days | 01 Feb 2027 | 08 Feb 2027 | 51SS+3 |
| 53 | Erection of steel beams and joists, Ground Floor | 7 days | 04 Feb 2027 | 11 Feb 2027 | 52SS+3 |
| 54 | Bolting, plumbing and final tightening, Ground Floor | 7 days | 08 Feb 2027 | 15 Feb 2027 | 53SS+3 |
| 55 | Steel stair stringers and treads, Ground Floor | 3 days | 16 Feb 2027 | 18 Feb 2027 | 54 |
| 56 | Reinforcement to staircase, Ground Floor | 3 days | 19 Feb 2027 | 22 Feb 2027 | 55 |
| 57 | Formwork to staircase, Ground Floor | 3 days | 20 Feb 2027 | 23 Feb 2027 | 56SS+1 |
| 58 | Inspection and approval of reinforcement, Ground Floor | 3 days | 22 Feb 2027 | 24 Feb 2027 | 57SS+1 |
| 59 | Concrete placement to staircase, Ground Floor | 3 days | 23 Feb 2027 | 25 Feb 2027 | 58SS+1 |
| 60 | Curing and striking of formwork to staircase, Ground Floor | 3 days | 24 Feb 2027 | 26 Feb 2027 | 59SS+1 |
| 61 | Balustrades and handrails to stairs, Ground Floor | 8 days | 27 Feb 2027 | 08 Mar 2027 | 60 |
| **62** | **FIRST FLOOR** | **21 days** | **16 Feb 2027** | **11 Mar 2027** | |
| 63 | Fabrication and delivery of structural steel, First Floor | 6 days | 16 Feb 2027 | 22 Feb 2027 | 43, 54 |
| 64 | Erection of steel columns, First Floor | 6 days | 19 Feb 2027 | 25 Feb 2027 | 63SS+3 |
| 65 | Erection of steel beams and joists, First Floor | 6 days | 23 Feb 2027 | 01 Mar 2027 | 64SS+3 |
| 66 | Bolting, plumbing and final tightening, First Floor | 6 days | 26 Feb 2027 | 04 Mar 2027 | 65SS+3 |
| 67 | Metal decking laying and fixing, First Floor | 5 days | 16 Feb 2027 | 20 Feb 2027 | 54 |
| 68 | Shear studs, edge trims and mesh, First Floor | 5 days | 19 Feb 2027 | 24 Feb 2027 | 67SS+3 |
| 69 | Reinforcement to suspended slab, First Floor | 3 days | 25 Feb 2027 | 27 Feb 2027 | 68 |
| 70 | Formwork to suspended slab, First Floor | 3 days | 27 Feb 2027 | 02 Mar 2027 | 69SS+2 |
| 71 | Inspection and approval of reinforcement, First Floor | 3 days | 02 Mar 2027 | 04 Mar 2027 | 70SS+2 |
| 72 | Concrete placement to suspended slab, First Floor | 3 days | 04 Mar 2027 | 06 Mar 2027 | 71SS+2 |

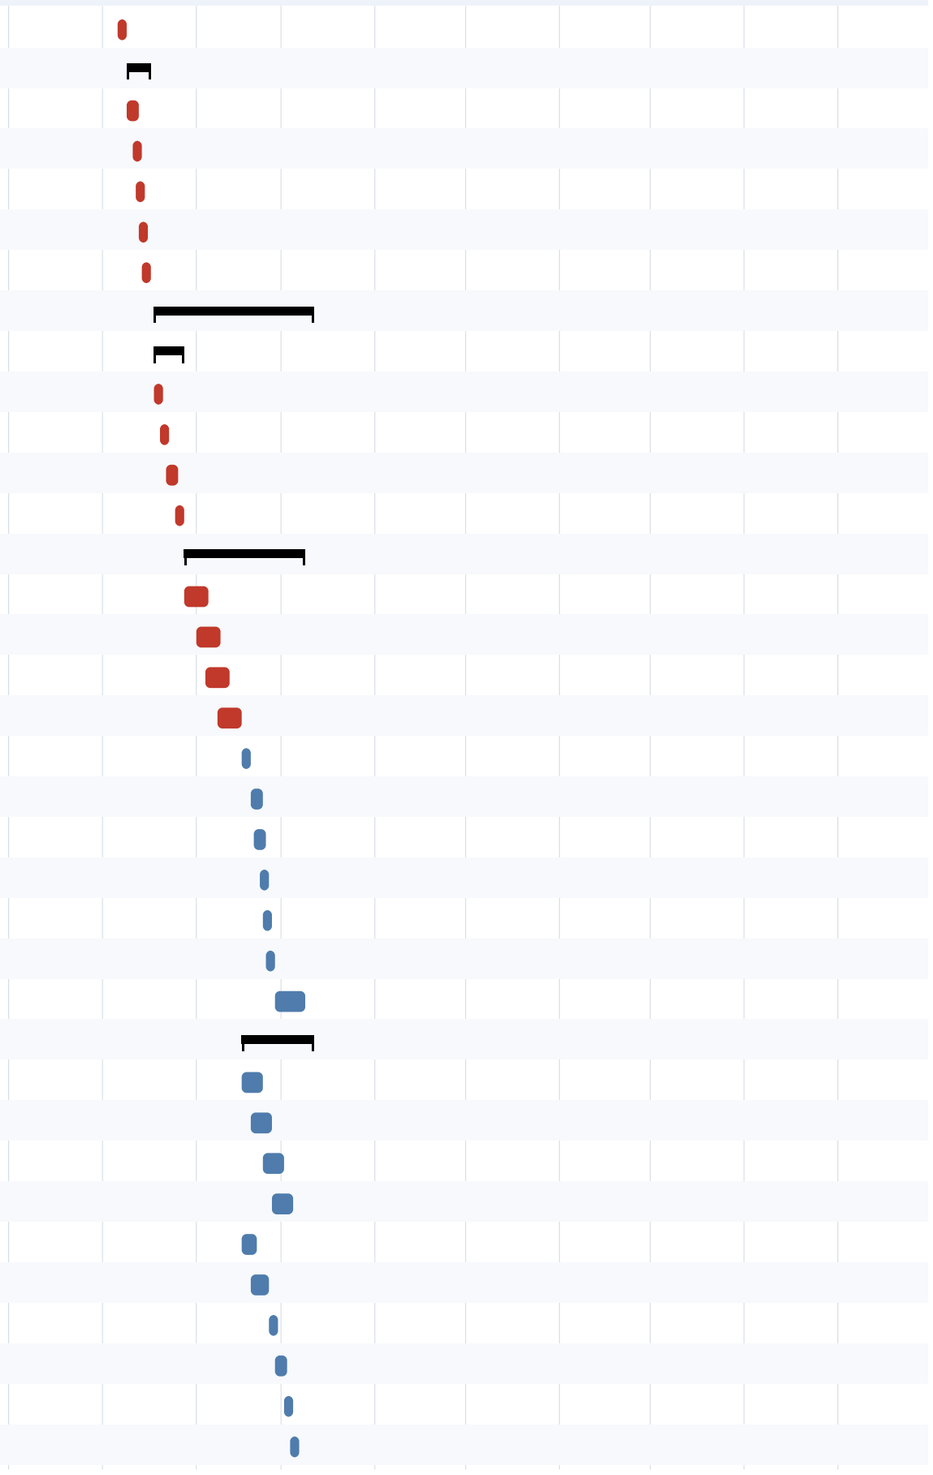

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 73 | Curing and striking of formwork to suspended slab, First Floor | 3 days | 06 Mar 2027 | 09 Mar 2027 | 72SS+2 |
| 74 | Balustrades and handrails to stairs, First Floor | 2 days | 10 Mar 2027 | 11 Mar 2027 | 66, 73 |
| **75** | **ROOF** | **8 days** | **08 Jul 2027** | **16 Jul 2027** | |
| 76 | Roof underlay and insulation | 4 days | 08 Jul 2027 | 12 Jul 2027 | 17, 127, 66 |
| 77 | Roof covering | 4 days | 10 Jul 2027 | 14 Jul 2027 | 76SS+2 |
| 78 | Flashings, upstands and roof outlets | 4 days | 13 Jul 2027 | 16 Jul 2027 | 77SS+2 |
| **79** | **WALLS AND PARTITIONS** | **118 days** | **16 Feb 2027** | **07 Jul 2027** | |
| **80** | **GROUND FLOOR** | **55 days** | **16 Feb 2027** | **22 Apr 2027** | |
| 81 | Setting out and first lift of walling, Ground Floor, zone A | 8 days | 16 Feb 2027 | 24 Feb 2027 | 54 |
| 82 | Setting out and first lift of walling, Ground Floor, zone B | 8 days | 19 Feb 2027 | 27 Feb 2027 | 81SS+3 |
| 83 | Blockwork and brickwork to full height, Ground Floor, zone A | 8 days | 23 Feb 2027 | 03 Mar 2027 | 82SS+3 |
| 84 | Blockwork and brickwork to full height, Ground Floor, zone B | 8 days | 26 Feb 2027 | 06 Mar 2027 | 83SS+3 |
| 85 | Lintels, stiffeners and wall plates, Ground Floor, zone A | 8 days | 02 Mar 2027 | 10 Mar 2027 | 84SS+3 |
| 86 | Lintels, stiffeners and wall plates, Ground Floor, zone B | 8 days | 05 Mar 2027 | 13 Mar 2027 | 85SS+3 |
| 87 | Head and base tracks, Ground Floor, zone A | 10 days | 16 Feb 2027 | 26 Feb 2027 | 54 |
| 88 | Head and base tracks, Ground Floor, zone B | 10 days | 22 Feb 2027 | 04 Mar 2027 | 87SS+5 |
| 89 | Stud framing to walls and partitions, Ground Floor, zone A | 10 days | 27 Feb 2027 | 10 Mar 2027 | 88SS+5 |
| 90 | Stud framing to walls and partitions, Ground Floor, zone B | 10 days | 05 Mar 2027 | 16 Mar 2027 | 89SS+5 |
| 91 | Boarding to first side, Ground Floor, zone A | 10 days | 17 Mar 2027 | 30 Mar 2027 | 86, 90 |
| 92 | Boarding to first side, Ground Floor, zone B | 10 days | 22 Mar 2027 | 03 Apr 2027 | 91SS+4 |
| 93 | Insulation and boarding to second side, Ground Floor, zone A | 10 days | 27 Mar 2027 | 08 Apr 2027 | 92SS+4 |
| 94 | Insulation and boarding to second side, Ground Floor, zone B | 10 days | 02 Apr 2027 | 13 Apr 2027 | 93SS+4 |
| 95 | Taping and jointing, Ground Floor, zone A | 10 days | 07 Apr 2027 | 17 Apr 2027 | 94SS+4 |
| 96 | Taping and jointing, Ground Floor, zone B | 10 days | 12 Apr 2027 | 22 Apr 2027 | 95SS+4 |
| **97** | **FIRST FLOOR** | **43 days** | **23 Apr 2027** | **14 Jun 2027** | |
| 98 | Setting out and first lift of walling, First Floor, zone A | 6 days | 23 Apr 2027 | 29 Apr 2027 | 96, 66, 73 |
| 99 | Setting out and first lift of walling, First Floor, zone B | 6 days | 27 Apr 2027 | 04 May 2027 | 98SS+3 |
| 100 | Blockwork and brickwork to full height, First Floor, zone A | 6 days | 30 Apr 2027 | 07 May 2027 | 99SS+3 |
| 101 | Blockwork and brickwork to full height, First Floor, zone B | 6 days | 05 May 2027 | 11 May 2027 | 100SS+3 |
| 102 | Lintels, stiffeners and wall plates, First Floor, zone A | 6 days | 08 May 2027 | 14 May 2027 | 101SS+3 |
| 103 | Lintels, stiffeners and wall plates, First Floor, zone B | 6 days | 12 May 2027 | 18 May 2027 | 102SS+3 |
| 104 | Head and base tracks, First Floor, zone A | 7 days | 23 Apr 2027 | 30 Apr 2027 | 96, 66, 73 |
| 105 | Head and base tracks, First Floor, zone B | 7 days | 27 Apr 2027 | 05 May 2027 | 104SS+3 |
| 106 | Stud framing to walls and partitions, First Floor, zone A | 7 days | 30 Apr 2027 | 08 May 2027 | 105SS+3 |
| 107 | Stud framing to walls and partitions, First Floor, zone B | 7 days | 05 May 2027 | 12 May 2027 | 106SS+3 |
| 108 | Boarding to first side, First Floor, zone A | 7 days | 19 May 2027 | 26 May 2027 | 103, 107 |

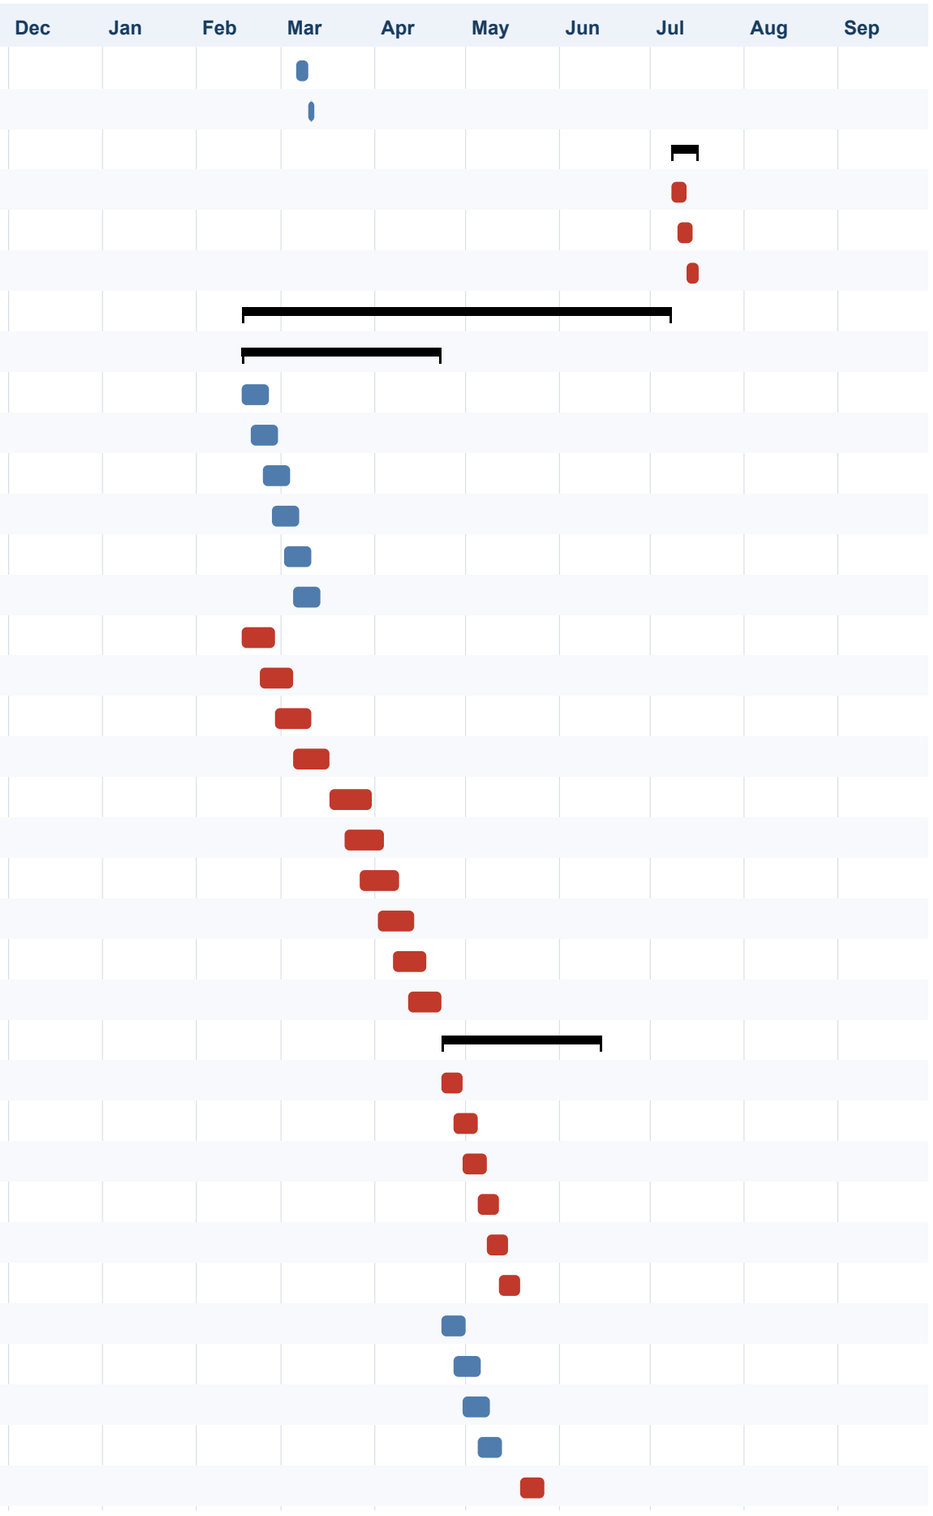


# PROGRAMME OF WORKS: LEKKI OFFICE BLOCK



Demo Partners QS  Contract period: 01 December 2026 to 30 September 2027 (10 months)  Monday to Saturday, Nigerian public holidays excluded  Revision B, 02 November 2026

Critical  With float

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 109 | Boarding to first side, First Floor, zone B | 7 days | 22 May 2027 | 29 May 2027 | 108SS+3 |
| 110 | Insulation and boarding to second side, First Floor, zone A | 7 days | 26 May 2027 | 02 Jun 2027 | 109SS+3 |
| 111 | Insulation and boarding to second side, First Floor, zone B | 7 days | 29 May 2027 | 05 Jun 2027 | 110SS+3 |
| 112 | Taping and jointing, First Floor, zone A | 7 days | 02 Jun 2027 | 09 Jun 2027 | 111SS+3 |
| 113 | Taping and jointing, First Floor, zone B | 7 days | 05 Jun 2027 | 14 Jun 2027 | 112SS+3 |
| **114** | **ROOF** | **20 days** | **15 Jun 2027** | **07 Jul 2027** | |
| 115 | Setting out and first lift of walling, Roof, zone A | 3 days | 15 Jun 2027 | 17 Jun 2027 | 113, 66, 73 |
| 116 | Setting out and first lift of walling, Roof, zone B | 3 days | 17 Jun 2027 | 19 Jun 2027 | 115SS+2 |
| 117 | Blockwork and brickwork to full height, Roof, zone A | 3 days | 19 Jun 2027 | 22 Jun 2027 | 116SS+2 |
| 118 | Blockwork and brickwork to full height, Roof, zone B | 3 days | 22 Jun 2027 | 24 Jun 2027 | 117SS+2 |
| 119 | Lintels, stiffeners and wall plates, Roof, zone A | 3 days | 24 Jun 2027 | 26 Jun 2027 | 118SS+2 |
| 120 | Lintels, stiffeners and wall plates, Roof, zone B | 3 days | 26 Jun 2027 | 29 Jun 2027 | 119SS+2 |
| 121 | Head and base tracks, Roof, zone A | 3 days | 15 Jun 2027 | 17 Jun 2027 | 113, 66, 73 |
| 122 | Head and base tracks, Roof, zone B | 3 days | 17 Jun 2027 | 19 Jun 2027 | 121SS+2 |
| 123 | Stud framing to walls and partitions, Roof, zone A | 3 days | 19 Jun 2027 | 22 Jun 2027 | 122SS+2 |
| 124 | Stud framing to walls and partitions, Roof, zone B | 3 days | 22 Jun 2027 | 24 Jun 2027 | 123SS+2 |
| 125 | Boarding to first side, Roof | 3 days | 30 Jun 2027 | 02 Jul 2027 | 124, 120 |
| 126 | Insulation and boarding to second side, Roof | 3 days | 02 Jul 2027 | 05 Jul 2027 | 125SS+2 |
| 127 | Taping and jointing, Roof | 3 days | 05 Jul 2027 | 07 Jul 2027 | 126SS+2 |
| **128** | **WINDOWS AND DOORS** | **51 days** | **23 Apr 2027** | **23 Jun 2027** | |
| **129** | **GROUND FLOOR** | **10 days** | **23 Apr 2027** | **05 May 2027** | |
| 130 | Window frames and subframes, Ground Floor, zone A | 3 days | 23 Apr 2027 | 26 Apr 2027 | 20, 96 |
| 131 | Window frames and subframes, Ground Floor, zone B | 3 days | 26 Apr 2027 | 28 Apr 2027 | 130SS+2 |
| 132 | Glazing and sealing of windows, Ground Floor, zone A | 3 days | 28 Apr 2027 | 30 Apr 2027 | 131SS+2 |
| 133 | Glazing and sealing of windows, Ground Floor, zone B | 3 days | 30 Apr 2027 | 04 May 2027 | 132SS+2 |
| 134 | Door frames and linings, Ground Floor, zone A | 4 days | 23 Apr 2027 | 27 Apr 2027 | 22, 96 |
| 135 | Door frames and linings, Ground Floor, zone B | 4 days | 26 Apr 2027 | 29 Apr 2027 | 134SS+2 |
| 136 | Hanging of doors and ironmongery, Ground Floor, zone A | 4 days | 28 Apr 2027 | 03 May 2027 | 135SS+2 |
| 137 | Hanging of doors and ironmongery, Ground Floor, zone B | 4 days | 30 Apr 2027 | 05 May 2027 | 136SS+2 |
| **138** | **FIRST FLOOR** | **8 days** | **15 Jun 2027** | **23 Jun 2027** | |
| 139 | Window frames and subframes, First Floor | 5 days | 15 Jun 2027 | 19 Jun 2027 | 113 |
| 140 | Glazing and sealing of windows, First Floor | 5 days | 18 Jun 2027 | 23 Jun 2027 | 139SS+3 |
| 141 | Door frames and linings, First Floor | 5 days | 15 Jun 2027 | 19 Jun 2027 | 113 |
| 142 | Hanging of doors and ironmongery, First Floor | 5 days | 18 Jun 2027 | 23 Jun 2027 | 141SS+3 |
| **143** | **FINISHES** | **11 days** | **17 Jul 2027** | **29 Jul 2027** | |
| **144** | **GROUND FLOOR** | **8 days** | **17 Jul 2027** | **26 Jul 2027** | |

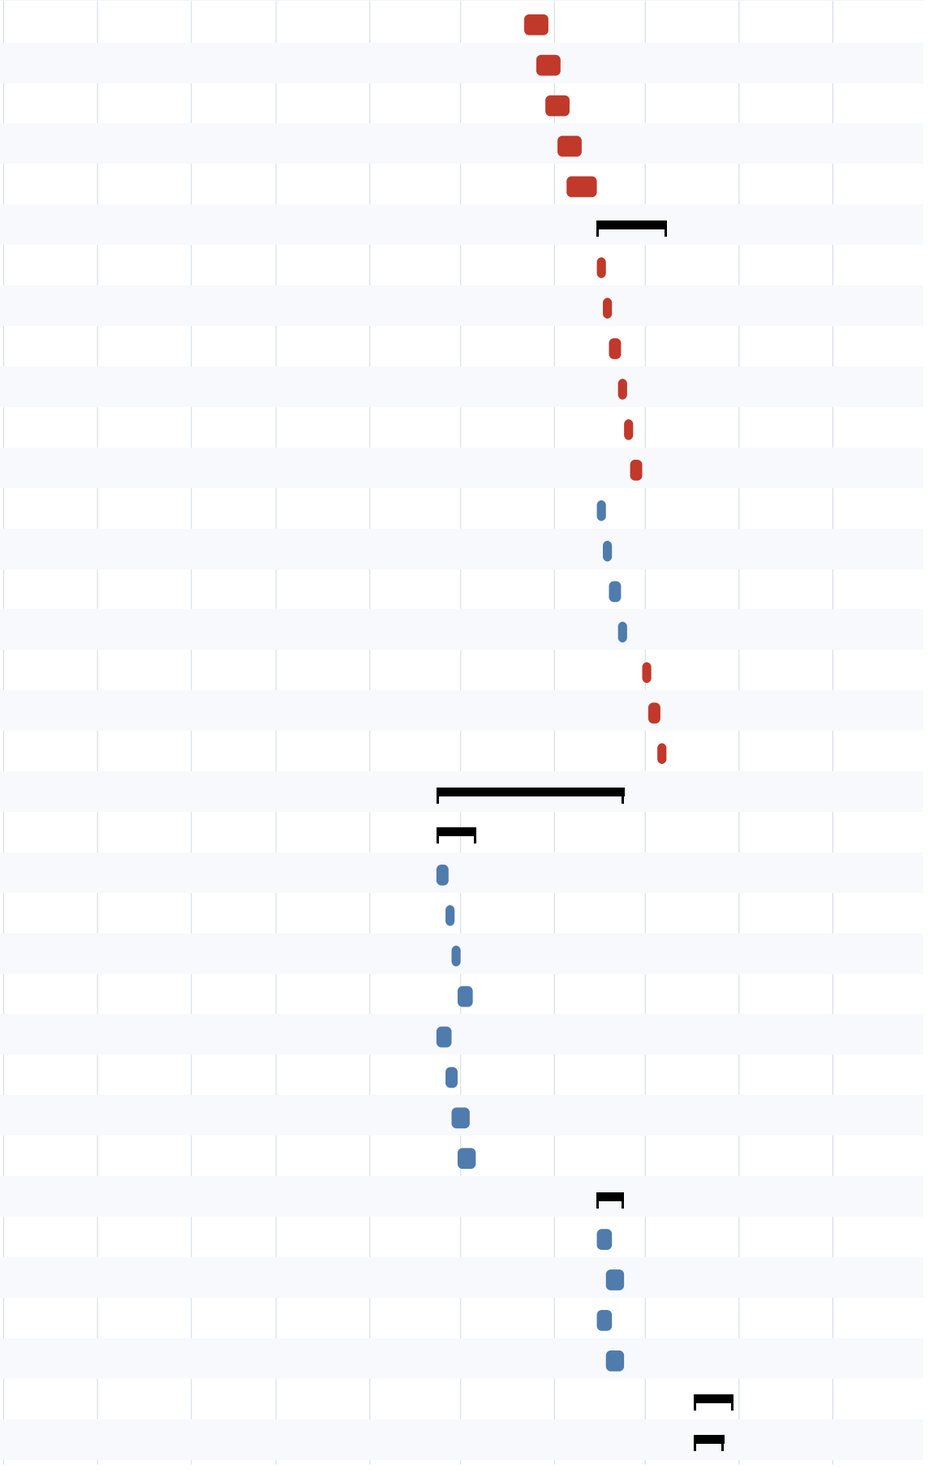


# PROGRAMME OF WORKS: LEKKI OFFICE BLOCK



Demo Partners QS  Contract period: 01 December 2026 to 30 September 2027 (10 months)  Monday to Saturday, Nigerian public holidays excluded  Revision B, 02 November 2026

Critical  With float

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 145 | Ceiling boards and tiles, Ground Floor | 5 days | 17 Jul 2027 | 22 Jul 2027 | 24, 78, 96 |
| 146 | Access panels and trims, Ground Floor | 5 days | 21 Jul 2027 | 26 Jul 2027 | 145SS+3 |
| 147 | Fittings and fixtures, Ground Floor | 3 days | 17 Jul 2027 | 20 Jul 2027 | 137, 78, 96 |
| **148** | **FIRST FLOOR** | **11 days** | **17 Jul 2027** | **29 Jul 2027** | |
| 149 | Ceiling suspension grid, First Floor | 2 days | 17 Jul 2027 | 19 Jul 2027 | 113, 78 |
| 150 | Ceiling boards and tiles, First Floor, zone A | 3 days | 20 Jul 2027 | 22 Jul 2027 | 149 |
| 151 | Ceiling boards and tiles, First Floor, zone B | 3 days | 22 Jul 2027 | 24 Jul 2027 | 150SS+2 |
| 152 | Access panels and trims, First Floor, zone A | 3 days | 24 Jul 2027 | 27 Jul 2027 | 151SS+2 |
| 153 | Access panels and trims, First Floor, zone B | 3 days | 27 Jul 2027 | 29 Jul 2027 | 152SS+2 |
| 154 | Fittings and fixtures, First Floor | 2 days | 17 Jul 2027 | 19 Jul 2027 | 113, 78, 142 |
| **155** | **M&E SERVICES** | **141 days** | **20 Feb 2027** | **07 Aug 2027** | |
| **156** | **GROUND FLOOR** | **9 days** | **27 Jul 2027** | **05 Aug 2027** | |
| 157 | Mechanical second fix: fittings and accessories, Ground Floor, zone A | 3 days | 27 Jul 2027 | 29 Jul 2027 | 81SS+4, 87SS+4, 78, 146 |
| 158 | Mechanical second fix: fittings and accessories, Ground Floor, zone B | 3 days | 29 Jul 2027 | 31 Jul 2027 | 157SS+2 |
| 159 | Mechanical equipment installation, Ground Floor, zone A | 3 days | 31 Jul 2027 | 03 Aug 2027 | 158SS+2 |
| 160 | Mechanical equipment installation, Ground Floor, zone B | 3 days | 03 Aug 2027 | 05 Aug 2027 | 159SS+2 |
| **161** | **ROOF** | **3 days** | **30 Jul 2027** | **02 Aug 2027** | |
| 162 | Mechanical second fix: fittings and accessories, Roof | 2 days | 30 Jul 2027 | 31 Jul 2027 | 121SS+4, 153, 78, 115SS+4 |
| 163 | Mechanical equipment installation, Roof | 2 days | 31 Jul 2027 | 02 Aug 2027 | 162SS+1 |
| **164** | **WHOLE BUILDING** | **141 days** | **20 Feb 2027** | **07 Aug 2027** | |
| 165 | Sanitary fittings and accessories | 3 days | 17 Jul 2027 | 20 Jul 2027 | 127, 78 |
| 166 | Plumbing second fix: fittings and accessories | 2 days | 30 Jul 2027 | 31 Jul 2027 | 153, 81SS+4, 87SS+4, 78 |
| 167 | Plumbing equipment installation | 2 days | 31 Jul 2027 | 02 Aug 2027 | 166SS+1 |
| 168 | Mechanical second fix: fittings and accessories | 5 days | 30 Jul 2027 | 04 Aug 2027 | 26, 153, 81SS+4, 87SS+4, 78 |
| 169 | Mechanical equipment installation | 5 days | 03 Aug 2027 | 07 Aug 2027 | 168SS+3 |
| 170 | Electrical first fix: conduits, sleeves and pipework, zone A | 18 days | 20 Feb 2027 | 12 Mar 2027 | 28, 81SS+4, 87SS+4 |
| 171 | Electrical first fix: conduits, sleeves and pipework, zone B | 18 days | 03 Mar 2027 | 23 Mar 2027 | 170SS+9 |
| 172 | Electrical first fix: cabling and draw wires, zone A | 18 days | 13 Mar 2027 | 05 Apr 2027 | 171SS+9 |
| 173 | Electrical first fix: cabling and draw wires, zone B | 18 days | 24 Mar 2027 | 15 Apr 2027 | 172SS+9 |
| 174 | Electrical second fix: fittings and accessories | 5 days | 30 Jul 2027 | 04 Aug 2027 | 153, 78, 173 |
| 175 | Electrical equipment installation | 5 days | 03 Aug 2027 | 07 Aug 2027 | 174SS+3 |
| 176 | Lift guide rails and car installation | 5 days | 17 Jul 2027 | 22 Jul 2027 | 30, 78 |
| 177 | Lift doors and landing fixtures | 5 days | 21 Jul 2027 | 26 Jul 2027 | 176SS+3 |
| **178** | **TESTING, COMMISSIONING AND HANDOVER** | **31 days** | **09 Aug 2027** | **13 Sep 2027** | |
| 179 | Electrical installation testing and certification | 8 days | 09 Aug 2027 | 17 Aug 2027 | 169, 160, 163, 175, 167, 177 |
| 180 | Mechanical systems commissioning and balancing | 10 days | 11 Aug 2027 | 21 Aug 2027 | 179SS+2 |

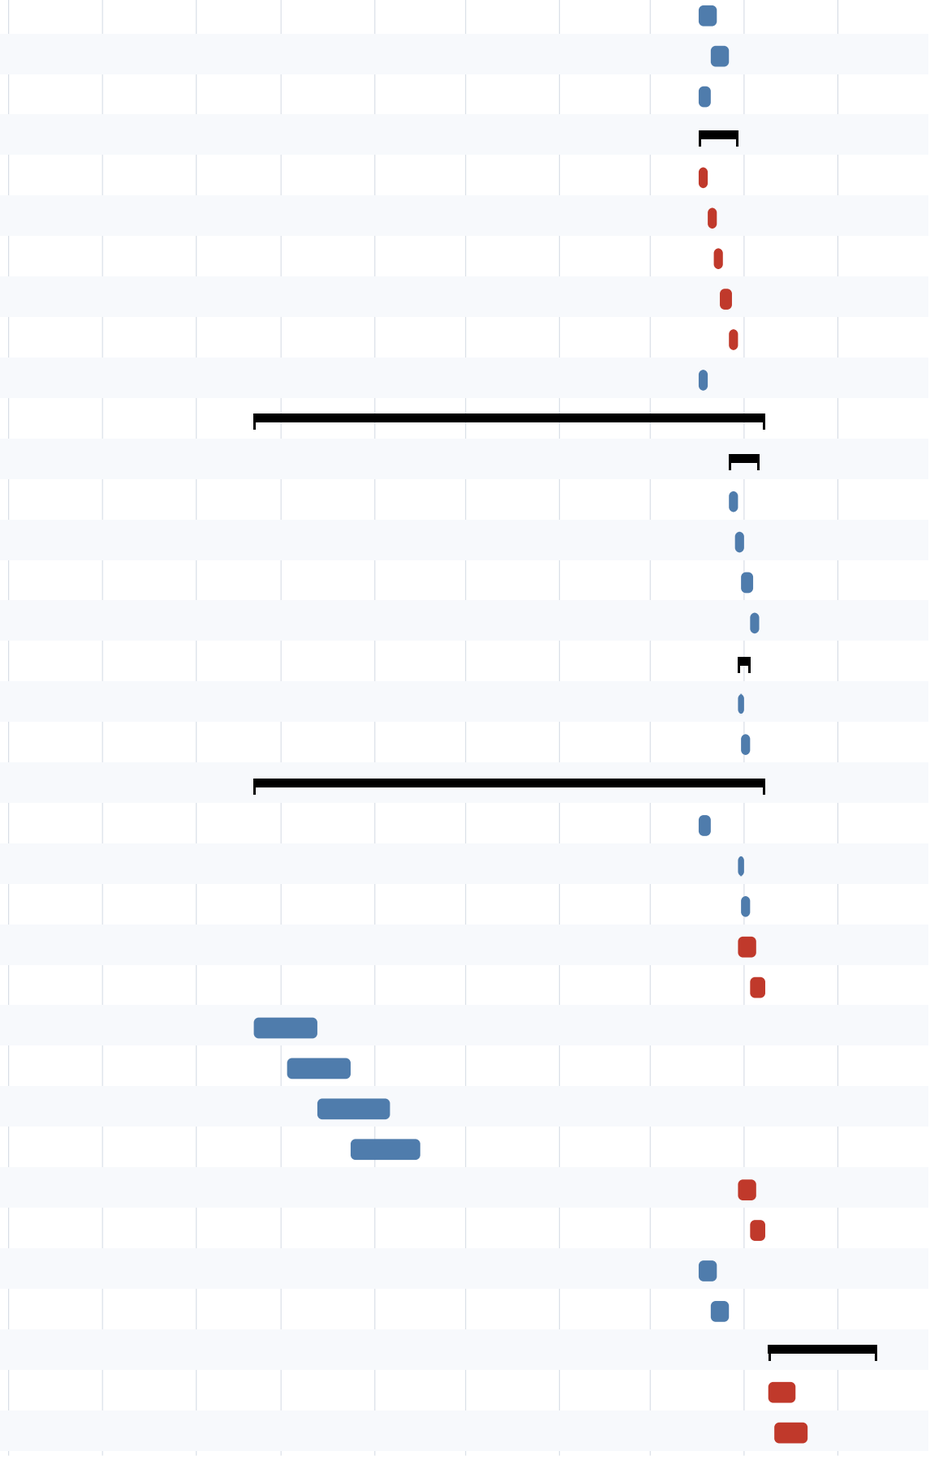

# PROGRAMME OF WORKS: LEKKI OFFICE BLOCK



Demo Partners QS  Contract period: 01 December 2026 to 30 September 2027 (10 months)  Monday to Saturday, Nigerian public holidays excluded  Revision B, 02 November 2026

Critical  With float

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 181 | Plumbing pressure testing and disinfection | 5 days | 13 Aug 2027 | 18 Aug 2027 | 180SS+2 |
| 182 | Lift testing and certification | 5 days | 16 Aug 2027 | 20 Aug 2027 | 181SS+2 |
| 183 | Snagging and rectification, Ground Floor | 4 days | 21 Aug 2027 | 25 Aug 2027 | 74, 147, 61, 133, 165, 140, 154, 182 |
| 184 | Snagging and rectification, First Floor | 4 days | 24 Aug 2027 | 27 Aug 2027 | 183SS+2 |
| 185 | Snagging and rectification, Roof | 4 days | 26 Aug 2027 | 30 Aug 2027 | 184SS+2 |
| 186 | Final builders clean | 5 days | 31 Aug 2027 | 04 Sep 2027 | 185 |
| 187 | O&M manuals, as-built drawings and handover documents | 5 days | 06 Sep 2027 | 10 Sep 2027 | 186 |
| 188 | Client inspection and handover | 2 days | 11 Sep 2027 | 13 Sep 2027 | 187 |
| **189** | **Practical completion** | **0 days** | **13 Sep 2027** | **13 Sep 2027** | **188** |

